



MANCHESTER PRIORITY ONE PROJECTS

OPM Monthly Project Report

Period Ending May 2024

Prepared for:



Joint School Buildings Committee

Prepared by:



Priority One Projects - Progress Graph Summary

Priority One Projects	Project Phase					
	Programming	Design	CM Procured	Bidding	Construction	Closeout
Modulars	100%	100%	100%	100%	<div></div> 20%	0%
Beech	85%	<div></div> 10%	<div></div> 30%	0%	0%	0%
McLaughlin	95%	<div></div> 30%	<div></div> 15%	0%	0%	0%
Hillside	95%	<div></div> 30%	<div></div> 15%	0%	0%	0%
Parkside	85%	<div></div> 20%	<div></div> 15%	0%	0%	0%
Southside	50%	<div></div> 20%	<div></div> 15%	0%	0%	0%

I. EXECUTIVE SUMMARY

LeftField was officially engaged on February 20th and has since immersed itself in the Priority One projects, focusing on gaining institutional knowledge on the pre-existing Priority One schedule, budget, and documentation. That said, LeftField has been actively refining the budget and schedule to establish a LeftField project standard, which is attached to this report. Please note that while the overall budget of 306 million will not change; however, there will be budgetary reclasses of costs within individual projects and from project to project. Additionally, LeftField has developed a series of individual project schedules for each of the six Priority One projects as well as an overall Priority One schedule, which are also attached to this report. Similarly, to the budget, the schedules are subject to change. LeftField has also assisted with developing a Criminal History Record Inquiry (CHRI) process and badging system that would comply with the District's existing policies and the construction industry. To date, the CHRI process and badging system have been implemented. Regular meetings with the District are ongoing to ensure comprehensive discussion and coordination of all project aspects.

The modular project proceeded forward in May with continued coordination with Triumph Modular and Consigli Construction. The delivery of 72 modular units to Manchester remains on schedule, with the first arrival of modulars delivered on May 23rd, with the remaining to follow. All modular units are expected to be delivered to Manchester by June 24th. In early May, Consigli Construction commenced with sitework, utilities, and site pad prep for the delivery and placement of the modular units. Consigli and the project team continue weekly communication with Eversource regarding power coordination for the various modular sites, which remains a critical path element to the modular projects.

LeftField has assisted the District with move coordination. Sterling Movers was retained by the District to manage the move from Wilson to the various modular locations. The District will coordinate internal school moves with assistance from the DPW through the vendors of Aramark and College Bound Movers. LeftField and SMMA have assisted the District with technology relocation and procurement, which will continue throughout the summer months. Various project permitting has continued and will remain a focus for the Priority One Projects.

Programming continues for the Middle School Projects and Beech Elementary. CM procurement continues for the middle school projects and the Beech Elementary School. The project team has met regularly to refine the schedules for the addition/renovations of the middle school projects.

For further details, please refer to the additional project information provided in the various sections of this report.

II. PROJECT PROCUREMENT

Architect/Engineer Procurement:

SMMA has been issued various amendments to their base contract for continued work associated with the Priority One Projects.

Owner's Project Manager Procurement:

On February 20th, the District officially engaged LeftField as their Owner's Project Manager ("OPM"). LeftField's contract has been fully executed as of the issuance of this report.

CM Procurement for the Modulares:

CM procurement for the modular project was completed with the CM Agreement Contract executed with Consigli on April 4th. The GMP amendment was drafted, and the final revision was submitted for acceptance and executed on May 2nd. R.S. Audley Inc. will be the site contractor, and Longchamps Electric Inc. will be the electrical contractor.

Sterling Movers:

LeftField assisted the District with move coordination and recommended engaging the services of Sterling Movers for the various moves related to the modular project/ site locations. The District is currently coordinating the contract between Sterling and the District.

III. PROJECT ACTIVITIES COMPLETED DURING MAY 2024

The following meetings/ Project activities occurred in May 2024:

- 05-01 Weekly Triumph Modular Coordination Meeting
 Weekly Consigli Coordination Meeting
 Weekly Priority One Project Meeting
- 05-02 Consigli Amendment #1/ GMP executed
- 05-02 Geotechnical exploratory work ongoing at Sheridan-Emmett Park,
 McLaughlin, and Hillside
- 05-03 Continued survey work conducted at Southside
- 05-06 Weekly LF Team coordination meeting
- 05-08 Weekly Triumph Modular Coordination Meeting
 Weekly Consigli Coordination Meeting

- Weekly Priority One Project Meeting
- JSBC Rpt 2 issued to the JSBC clerk; distributed to the JSBC on 05-09
- 05-13 Weekly LF Team coordination meeting
- CM RFQ posted for Beech Street Project
- 05-14 JSBC Meeting
- 05-14 Project team coordination mtg to discuss middle school schedules
- 05-15 Weekly Triumph Modular Coordination Meeting
- Weekly Consigli Coordination Meeting
- Weekly Priority One Project Meeting
- Traffic survey conducted at Hillside, McLaughlin, and Beech
- 05-16 CM RFQ's received by the District
- 05-20 Weekly LF Team coordination meeting
- 05-22 Weekly Triumph Modular Coordination Meeting
- Weekly Consigli Coordination Meeting
- Weekly Priority One Project Meeting
- District reviews the CM qualifications received and decides to readvertise the RFQ for the Middle Schools
- 05-23 School tours conducted
- District issues letter to Amoskeag Board explaining the Beech Elementary school project and land swap intent. *
- 05-24 LeftField provided a cursory MEP walk-through for Hillside & McLaughlin
- 05-27 Weekly LF Team coordination meeting
- 05-29 Weekly Triumph Modular Coordination Meeting
- Weekly Consigli Coordination Meeting
- Weekly Priority One Project Meeting
- 05-30 Project Team meeting regarding communication
- City and District personnel met with the State regarding LWCF conditions/restrictions for various school and city-controlled properties **
- 05-31 Southside Gas Line meeting with Liberty and Project Team

* Additional information will follow via Mr. James O'Connell.

** As a result of the meeting held, it was determined that all applicable priority one properties subject to LWCF restrictions will be adjusted through an application process, which will be orchestrated by legal counsel. Based on the aforementioned, the project[s] were authorized to proceed forward.

IV. ACTIVITIES PLANNED FOR JUNE 2024

The following meetings/ activities are planned for June 2024:

- 06-04 Liberty gas coordination meeting
- 06-05 Attendance to seminar held by NH Department of Education re:
state funding
Weekly Triumph Modular Coordination Meeting
Weekly Consigli meeting
Weekly Project Meeting
- 06-06 Issue monthly Rpt 3 and draft slide deck to the JSBC clerk
- 06-07 JSBC clerk issues monthly Rpt 3 and draft side deck to the JSBC
- 06-10 LeftField Team Weekly coordination meeting
- 06-12 Weekly Triumph Modular Coordination Meeting
Weekly Consigli meeting
Weekly Project Meeting
- 06-14 CM RFQ Statement of Qualifications due
- 06-17 LeftField Team Weekly coordination meeting
- 06-19 Weekly Triumph Modular Coordination Meeting
Weekly Consigli meeting
Weekly Project Meeting
Project Team meeting to coordinate middle school schedules
- 06-24 LeftField Team Weekly coordination meeting
- 06-26 Weekly Triumph Modular Coordination Meeting
Weekly Consigli meeting
Weekly Project Meeting
- Continued Deliveries of Modulares
- Security Coordination of Modulares
- Continued coordination of move activities
- Continued coordination of technology for the modulares

Please note additional activities and meetings will occur that have not been scheduled as of the issuance of this report. In addition, the above meetings are subject to change.

V. PROJECT BUDGET & INVOICING

LeftField has been forwarded the existing \$306M budget, previously established before LeftField's engagement. LeftField has developed and implemented the 306-million-dollar budget into a LeftField formatted standard. A summary of all six projects and individual

project budgets can be found in Attachment A of this report. **Please note that this budget remains a work in progress. LeftField will be amending the budget based on a more thorough review of existing allocated project costs and anticipated project cost reallocations based on an individual budget line-item analysis.**

The recommended invoice approval process developed by LeftField and the District is working effectively, and billing and payment cycles have occurred to date. All invoices continue to be sent to LeftField and reviewed by the appropriate project team members. The contractor payment requisition is being reviewed by LeftField and SMMA and certified for payment by SMMA. LeftField has codified all invoices into a batch/ log with associated backup. The invoice log with backup is being signed as 'recommended for payment' by LeftField and issued to the District CFO and the Superintendent of Schools for signature. The CFO will then process payment accordingly based on the current schedule of Finance Warrant signing dates. Attachment B of this report shows the invoice log for the period ending May 2024. **Please note that this payment log is scheduled for District approval on June 7th and payment approval on June 13th, with the payment check date for June 14th. Due to the timing of this report and the aforementioned dates, the May invoice log/batch has been included in the attached budget as encumbered/expended.**

Change Orders Events to Date as of the Issuance of this Report:

Vendor	Value	Description
Triumph Modular		
PCO 2	\$ (217,335)	Change from concrete footing system to metal plate foundation system
PCO 3	\$ 169,650	Associated grading and ramp changes
Subtotal	\$ (47,685)	This is reflective in the budget
Consigli Construction		
CO 1	\$ (21,539)	Finalization of alternates
Subtotal	\$ (21,539)	This will be reflective in the budget for next month
Total	\$ (69,224)	

VI. PROJECT SCHEDULE

LeftField has been developing the existing schedule. LeftField has transferred the received schedule into a LeftField formatted schedule. A summary of all six project schedules' rolled up' and individual project schedules can be found in Attachment C of this report. **Please note that the individual schedules and overall 'rolled up' schedule remains a work in progress. LeftField will be amending the individual project schedules based on a more thorough review of each individual project and anticipated scope.**

The modular project is currently on schedule. However, the availability and delivery of the Eversource pad-mounted transformers remain critical path activities. **To date, the**

project team consisting of SMMA and their engineers, Consigli and their trade partners, the School District and staff members, and utility companies have all been extremely accommodating with each other to allow various construction activities to pivot as required based on unforeseen conditions that occur daily in the design/construction industry.

Regarding the Middle School Projects, the project team has been meeting to review the timeline and phasing options for the middle school projects.

Programming for the Middle Schools and Beech has continued throughout May.

MODULAR PROJECT

SUMMARY PROGRESS GRAPH

Modulars	Project Phase									
	Modular Units Fabricated	Modular Units Infrastructure	Modular Units Delivered	Modular Units Set	Modular Unit MEP Connections	General Sitework	Eversource Power	FA, Security, Certificate of Occupancy Testing	Modular Furniture, Equipment & Technology	Closeout
Beech	100%	100%	100%	0%	0%	75%	10%	0%	25%	0%
McDonough	90%	60%	0%	0%	0%	60%	10%	0%	25%	0%
McLaughlin	100%	85%	100%	100%	0%	60%	10%	0%	25%	0%
Hillside	100%	0%	0%	0%	0%	10%	10%	0%	25%	0%
Parkside	50%	0%	0%	0%	0%	10%	10%	0%	25%	0%
Southside	100%	0%	100%	0%	0%	10%	10%	0%	25%	0%

Modulars	Eversource Journey To Permanent Power						
	Site walk	Design	Pole Pad mounted	Work Orders Issued	Confirmation of Delivery *	Transformers, Cabinets ** Delivered	Power Terminated
Beech	100%	100%	Pole	100%	100%	0%	0%
McDonough	100%	100%	Pole	100%	100%	0%	0%
McLaughlin	100%	100%	Pad	100%	0%	0%	0%
Hillside	100%	100%	Pad	100%	0%	0%	0%
Parkside	100%	100%	Pole	100%	100%	0%	0%
Southside	100%	100%	Pad	100%	0%	0%	0%

* Estimated confirmation of lead times TBD.

** CT cabinets for McDonough, McLaughlin, Hillside, and Southside have been picked up from Eversource.

Construction-Related Activities During May 2024:

Beech

- Erosion control and fencing installed
- Limited sitework-related demolition for utilities
- Sewer work and water line installed
- Modular pad prepared



Beech Street Modular Pad Prepared

Southside

- Erosion control and fencing installed
- Engineering and layout completed for modulares
- Ongoing coordination regarding gas line relocation



Southside Modulares Delivered; awaiting for final set and installation

Hillside

- Site fencing installed
- Site contractor mobilized

McLaughlin

- Erosion control and fencing installed
- Limited sitework-related demolition for utilities
- Sewer work and water line installed
- Relocate existing light poles
- Remove loam, install new driveway
- Modular pad prepared
- Modulares set on June 1st and 2nd.



McLaughlin Modulares set; additional work to follow...

Parkside:

- Install temp fencing
- Dig safe mark out complete
- Engineering and layout of pad complete
- Relocation of gas service coordinated with Liberty

McDonough:

- Erosion control and fencing installed
- Limited sitework-related demolition for utilities
- Sewer work and water line installed
- U/G electrical work installed
- Waiting for pole mounted transformers and CT Cabinet



Pad prepared ready for modular units



U/G Electrical work from CT cabinet to future pole-mounted transformers

Next 30 days:Beech:

- Site Lighting
- Set utility poles
- Receive & set Modulars
- Complete U/G electrical
- Site restoration
- Fiber installation

McDonough:

- U/G electrical work
- Prep Mod pad
- Start playground
- Start retaining wall
- Relocate Basketball hoops
- Start parking lot
- Receive Modulars

Hillside:

- Sewer work
- Erosion control
- Limited demolition
- Start rip rap embankment
- Tie-in water service
- U/G electrical for light poles
- Prep pad for Modulars
- Receive Modulars
- Installation of poles for power

McLaughlin:

- Paving & landscape restoration
- U/G electrical
- Install transformer pad
- Fiber installation

Southside:

- Erosion control
- Limited site demolition
- Sewer work

- U/G electrical
- Prep pad
- Install water line
- Install gas line
- Set modulars

Parkside:

- Sewer work
- Prep pad
- Limited demolition for utilities
- Water line work
- Relocation of gas line

Middle School Projects

Upcoming Activities

- CMR Procurement ongoing
- Phasing and middle school construction schedule ongoing

Beech Elementary

Upcoming Activities

- CMR Procurement ongoing

VII. ATTACHMENTS

- | | |
|----------------|--|
| • Attachment A | LeftField Budget [subject to further review & modifications] |
| • Attachment B | Invoice Log for the period ending May 2024 |
| • Attachment C | LeftField Schedule [subject to further review & modifications] |
| • Attachment D | Modular Delivery Schedule [subject to change] |

VIII. PROJECT OUTREACH / COMMUNICATION

Project-related records such as agendas, agenda packets, and minutes can be viewed via this link:

<https://www.manchesternh.gov/Departments/City-Clerk/Meeting-Minutes-and-Agendas/Current>

Official upcoming meeting postings [date/time] can be viewed via this link:

<https://www.mansd.org/o/msd/page/calendar-bosc>
<https://www.manchesternh.gov/Government/City-Calendars>

ATTACHMENT A

Priority One Budget Rolled-Up Summary
Individual Project Budgets - Detail

Manchester Priority One Projects - Overall Budget Summary

Manchester School District - Priority One Projects

Period Ending
Invoice Summary Package

5/31/2024
4

Current Budget



	Original Budget [A]	Budget Changes [B]	Current Budget [C]	Committed Costs [D]	Expended [E]	Unspent [F]=[D]-[E]	Remaining Budget [G]=[C]-[D]	CTC (beyond committed) [I]	Anticipated C @ C [J]=[D]+[I]	Variance (Under) / Over [K]=[D]-[J]
MODULAR PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$253,077	\$0	\$253,077	\$245,077	\$110,314	\$134,763	\$8,000	\$8,000	\$253,077	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$1,690,143	\$0	\$1,690,143	\$1,690,143	\$1,309,956	\$380,187	\$0	\$0	\$1,690,143	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$5,560,000	\$64,958	\$5,624,958	\$5,624,958	\$1,200,704	\$4,424,254	\$0	\$0	\$5,624,958	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$17,170,000	(\$221,869)	\$16,948,131	\$16,705,437	\$1,591,147	\$15,114,290	\$242,694	\$242,694	\$16,948,131	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$604,000	\$0	\$604,000	\$0	\$0	\$0	\$604,000	\$604,000	\$604,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$965,270	\$156,911	\$1,122,181	\$0	\$0	\$0	\$1,122,181	\$1,122,181	\$1,122,181	\$0
MODULAR PROJECT TOTALS	\$26,242,490	\$0	\$26,242,490	\$24,265,615	\$4,212,121	\$20,053,494	\$1,976,875	\$1,976,875	\$26,242,490	\$0
BEECH STREET ELEMENTARY SCHOOL PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$2,057,129	\$250,000	\$2,307,129	\$2,176,071	\$30,992	\$2,145,079	\$131,058	\$131,058	\$2,307,129	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$5,095,000	\$0	\$5,095,000	\$4,945,000	\$291,287	\$4,653,713	\$150,000	\$150,000	\$5,095,000	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$58,196,935	\$0	\$58,196,935	\$0	\$0	\$0	\$58,196,935	\$58,196,935	\$58,196,935	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$450,000	\$0	\$450,000	\$0	\$0	\$0	\$450,000	\$450,000	\$450,000	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$2,348,800	\$0	\$2,348,800	\$0	\$0	\$0	\$2,348,800	\$2,348,800	\$2,348,800	\$0
0800 0000 OWNER'S CONTINGENCY	\$5,963,970	(\$250,000)	\$5,713,970	\$0	\$0	\$0	\$5,713,970	\$5,713,970	\$5,713,970	\$0
BEECH STREET ELEMENTARY SCHOOL PROJECT TOTALS	\$74,111,834	\$0	\$74,111,834	\$7,121,071	\$322,279	\$6,798,792	\$66,990,763	\$66,990,763	\$74,111,834	\$0
HILLSIDE MIDDLE SCHOOL PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,017,155	\$0	\$1,017,155	\$976,626	\$33,340	\$943,285	\$40,529	\$40,529	\$1,017,155	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$4,087,500	\$0	\$4,087,500	\$3,937,500	\$305,743	\$3,631,757	\$150,000	\$150,000	\$4,087,500	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$43,527,708	\$0	\$43,527,708	\$0	\$0	\$0	\$43,527,708	\$43,527,708	\$43,527,708	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$0	\$250,000	\$250,000	\$250,000	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$3,520,000	\$0	\$3,520,000	\$0	\$0	\$0	\$3,520,000	\$3,520,000	\$3,520,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$4,601,489	\$0	\$4,601,489	\$0	\$0	\$0	\$4,601,489	\$4,601,489	\$4,601,489	\$0
HILLSIDE MIDDLE SCHOOL PROJECT TOTALS	\$57,003,852	\$0	\$57,003,852	\$4,914,126	\$339,083	\$4,575,042	\$52,089,726	\$52,089,726	\$57,003,852	\$0
MCLAUGHLIN MIDDLE SCHOOL PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,017,155	\$0	\$1,017,155	\$976,626	\$32,053	\$944,573	\$40,529	\$40,529	\$1,017,155	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$3,232,500	\$0	\$3,232,500	\$3,082,500	\$243,473	\$2,839,027	\$150,000	\$150,000	\$3,232,500	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$28,827,403	\$0	\$28,827,403	\$0	\$0	\$0	\$28,827,403	\$28,827,403	\$28,827,403	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$0	\$250,000	\$250,000	\$250,000	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$3,200,000	\$0	\$3,200,000	\$0	\$0	\$0	\$3,200,000	\$3,200,000	\$3,200,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$3,161,130	\$0	\$3,161,130	\$0	\$0	\$0	\$3,161,130	\$3,161,130	\$3,161,130	\$0
MCLAUGHLIN MIDDLE SCHOOL PROJECT TOTALS	\$39,688,188	\$0	\$39,688,188	\$4,059,126	\$275,526	\$3,783,600	\$35,629,062	\$35,629,062	\$39,688,188	\$0
PARKSIDE MIDDLE SCHOOL PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,101,287	\$0	\$1,101,287	\$1,057,381	\$35,663	\$1,021,718	\$43,907	\$43,907	\$1,101,287	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$3,927,500	\$0	\$3,927,500	\$3,777,500	\$38,400	\$3,739,100	\$150,000	\$150,000	\$3,927,500	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$36,146,140	\$0	\$36,146,140	\$0	\$0	\$0	\$36,146,140	\$36,146,140	\$36,146,140	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$0	\$250,000	\$250,000	\$250,000	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$3,200,000	\$0	\$3,200,000	\$0	\$0	\$0	\$3,200,000	\$3,200,000	\$3,200,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$3,877,019	\$0	\$3,877,019	\$0	\$0	\$0	\$3,877,019	\$3,877,019	\$3,877,019	\$0
PARKSIDE MIDDLE SCHOOL PROJECT TOTALS	\$48,501,946	\$0	\$48,501,946	\$4,834,881	\$74,063	\$4,760,818	\$43,667,066	\$43,667,066	\$48,501,946	\$0
SOUTHSIDE MIDDLE SCHOOL PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,101,287	\$0	\$1,101,287	\$1,057,381	\$33,450	\$1,023,930	\$43,907	\$43,907	\$1,101,287	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$4,317,500	\$0	\$4,317,500	\$4,167,500	\$43,200	\$4,124,300	\$150,000	\$150,000	\$4,317,500	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$46,685,769	\$0	\$46,685,769	\$0	\$0	\$0	\$46,685,769	\$46,685,769	\$46,685,769	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$0	\$250,000	\$250,000	\$250,000	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$3,200,000	\$0	\$3,200,000	\$0	\$0	\$0	\$3,200,000	\$3,200,000	\$3,200,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$4,897,135	\$0	\$4,897,135	\$0	\$0	\$0	\$4,897,135	\$4,897,135	\$4,897,135	\$0
SOUTHSIDE MIDDLE SCHOOL PROJECT TOTALS	\$60,451,691	\$0	\$60,451,691	\$5,224,881	\$76,650	\$5,148,230	\$55,226,811	\$55,226,811	\$60,451,691	\$0
GRAND TOTAL MANCHESTER PRIORITY ONE PROJECTS	\$306,000,000	\$0	\$306,000,000	\$50,419,698	\$5,299,723	\$45,119,976	\$255,580,302	\$255,580,302	\$306,000,000	\$0

Manchester School District - Modular Project



Manchester School District - Modular Project
Project Director / Manager: David Saindon / Mark Lenfest

Period Ending 5/31/2024
Invoice Summary Package 4
Includes GC/CM Requisition N/A

Current Budget



	Original Budget [A]	Budget Reallocations [B]	Current Budget [C]	Committed Costs [D]	Expended [E]	Unspent [F]=[D]-[E]	Remaining Budget [G]=[C]-[D]	% Complete (against commit'd) [H]=[E]/[J]	CTC (beyond committed) [I]	Anticipated C @ C [J]=[D]+[I]	Variance (Under) / Over [K]=[C]-[J]
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$253,077	\$0	\$253,077	\$245,077	\$110,314	\$134,763	\$8,000		\$8,000	\$253,077	\$0
0101 0000 Legal Fees	\$8,000	\$0	\$8,000	\$0	\$0	\$0	\$8,000		\$8,000	\$8,000	\$0
0102 0000 Owner's Project Manager (Leftfield)											
0102 0400 Design Development	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 0500 Construction Contract Docs	\$20,611	\$0	\$20,611	\$20,611	\$18,304	\$2,307	\$0	89%	\$0	\$20,611	\$0
0102 0600 Bidding	\$20,611	\$0	\$20,611	\$20,611	\$20,611	\$0	\$0	100%	\$0	\$20,611	\$0
0102 0700 Construction Contract Administration	\$203,855	\$0	\$203,855	\$203,855	\$71,399	\$132,456	\$0	35%	\$0	\$203,855	\$0
0102 0800 Closeout	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0103 0000 Advertising	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0104 0000 Permitting Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0105 0000 Owner's Insurance	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Other Administrative Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$1,690,143	\$0	\$1,690,143	\$1,690,143	\$1,309,956	\$380,187	\$0		\$0	\$1,690,143	\$0
0201 0000 Basic Services (SMMa)											
0201 0400 Design Development / Programming / RFP	\$216,000	\$0	\$216,000	\$216,000	\$216,000	\$0	\$0	100%	\$0	\$216,000	\$0
0201 0500 Construction Contract Documents / Site Package	\$480,000	\$0	\$480,000	\$480,000	\$480,000	\$0	\$0	100%	\$0	\$480,000	\$0
0201 0600 Bidding	\$96,000	\$0	\$96,000	\$96,000	\$96,000	\$0	\$0	100%	\$0	\$96,000	\$0
0201 0700 Construction Contract Administration	\$408,000	\$0	\$408,000	\$408,000	\$102,000	\$306,000	\$0	25%	\$0	\$408,000	\$0
0201 0800 Closeout	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 0000 Reimbursable and Other Services											
0203 0200 Printing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Other Reimbursable Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0000 Sub-Consultants											
0204 0200 Hazardous Materials	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0300 GeoTechnical & Geo-Environmental	\$106,100	\$0	\$106,100	\$106,100	\$56,100	\$50,000	\$0	53%	\$0	\$106,100	\$0
0204 0400 Site Survey	\$365,750	\$0	\$365,750	\$365,750	\$359,856	\$5,894	\$0	98%	\$0	\$365,750	\$0
0204 0400 Site Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0500 Wetlands	\$18,293	\$0	\$18,293	\$18,293	\$0	\$18,293	\$0	0%	\$0	\$18,293	\$0
0204 1200 Traffic Studies	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0300 0000 SITE ACQUISITION IN/AI	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$5,560,000	\$64,958	\$5,624,958	\$5,624,958	\$1,200,704	\$4,424,254	\$0		\$0	\$5,624,958	\$0
0501 0000 Pre-Construction Services	\$60,000	(\$44,640)	\$15,360	\$15,360	\$15,360	\$0	\$0	100%	\$0	\$15,360	\$0
0502 0000 Construction											
0502 0000 Construction Budget	\$5,500,000	\$109,598	\$5,609,598	\$5,609,598	\$1,185,344	\$4,424,254	\$0	21%	\$0	\$5,609,598	\$0
0508 0000 Change Orders	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$17,170,000	(\$221,869)	\$16,948,131	\$16,705,437	\$1,591,147	\$15,114,290	\$242,694		\$242,694	\$16,948,131	\$0
0601 0000 Utility Company Fees	\$120,000	\$0	\$120,000	\$87,306	\$87,306	\$0	\$32,694	100%	\$32,694	\$120,000	\$0
0602 0000 Testing Services	\$50,000	(\$40,000)	\$10,000	\$0	\$0	\$0	\$10,000		\$10,000	\$10,000	\$0
0603 0000 Swing Space/Modulars	\$16,800,000	(\$134,184)	\$16,665,816	\$16,665,816	\$1,503,841	\$15,161,975	\$0	9%	\$0	\$16,665,816	\$0
0604 0000 Change Orders - Modulars	\$0	(\$47,685)	(\$47,685)	(\$47,685)	\$0	(\$47,685)	\$0	0%	\$0	(\$47,685)	\$0
0699 0000 Other Project Costs (Moving, etc.)	\$200,000	\$0	\$200,000	\$0	\$0	\$0	\$200,000		\$200,000	\$200,000	\$0
0699 0000 Stipend for Teacher Move	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$604,000	\$0	\$604,000	\$0	\$0	\$0	\$604,000		\$604,000	\$604,000	\$0
0701 0000 Furnishings & Equipment (FF+E)	\$112,000	\$0	\$112,000	\$0	\$0	\$0	\$112,000		\$112,000	\$112,000	\$0
0703 0000 Technology	\$492,000	\$0	\$492,000	\$0	\$0	\$0	\$492,000		\$492,000	\$492,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$965,270	\$156,911	\$1,122,181	\$0	\$0	\$0	\$1,122,181		\$1,122,181	\$1,122,181	\$0
0801 0000 Owner's Contingency (soft)	\$163,958	\$0	\$163,958	\$0	\$0	\$0	\$163,958		\$163,958	\$163,958	\$0
0507 0000 Owner's Construction Contingency (hard)	\$801,312	\$156,911	\$958,223	\$0	\$0	\$0	\$958,223		\$958,223	\$958,223	\$0
PROJECT TOTALS	\$26,242,490	\$0	\$26,242,490	\$24,265,615	\$4,212,121	\$20,053,494	\$1,976,875		\$1,976,875	\$26,242,490	\$0

Manchester School District - Beech Street Elementary School Project



Manchester School District - Beech Street Elementary School Project
Project Director / Manager: David Saindon / Hamdi Cobanoglu

Period Ending
Invoice Summary Package
Includes GC/CM Requisition

5/31/2024
4
N/A

Current Budget



	Original Budget (A)	Budget Changes (B)	Current Budget (C)	Committed Costs (D)	Expended (E)	Unspent (F)=(D)-(E)	Remaining Budget (G)=(C)-(D)	% Complete (against committed) (H)=(E)/(J)	CTC (beyond committed) (I)	Anticipated C @ C (J)=(D)+(I)	Variance (Under) / Over (K)=(C)-(J)
0100 0000 ADMINISTRATION	\$2,057,129	\$250,000	\$2,307,129	\$2,176,071	\$30,992	\$2,145,079	\$131,058		\$131,058	\$2,307,129	\$0
0101 0000 Legal Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 0000 Owner's Project Manager (Leftfield)											
0102 0100 Programming/Feasibility/Schematic Design	\$173,979	\$0	\$173,979	\$173,979	\$30,992	\$142,987	\$0	18%	\$0	\$173,979	\$0
0102 0400 Design Development	\$74,563	\$0	\$74,563	\$74,563	\$0	\$74,563	\$0	0%	\$0	\$74,563	\$0
0102 0500 Construction Contract Docs	\$99,417	\$0	\$99,417	\$99,417	\$0	\$99,417	\$0	0%	\$0	\$99,417	\$0
0102 0600 Bidding	\$50,055	\$0	\$50,055	\$50,055	\$0	\$50,055	\$0	0%	\$0	\$50,055	\$0
0102 0700 Construction Contract Administration	\$1,546,243	\$0	\$1,546,243	\$1,465,185	\$0	\$1,465,185	\$81,058	0%	\$81,058	\$1,546,243	\$0
0102 0800 Closeout	\$62,872	\$0	\$62,872	\$62,872	\$0	\$62,872	\$0	0%	\$0	\$62,872	\$0
0102 0900 Extra Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1000 Reimbursable & Other Services (Cookson Communications)	\$0	\$250,000	\$250,000	\$250,000	\$0	\$250,000	\$0	0%	\$0	\$250,000	\$0
0102 1100 Cost Estimates	\$50,000	\$0	\$50,000	\$0	\$0	\$0	\$50,000		\$50,000	\$50,000	\$0
0102 9900 Other Project Manager Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0103 0000 Advertising	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0104 0000 Permitting Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0105 0000 Owner's Insurance	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Other Administrative Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Structural Peer Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Scope of Site Plan & Special Permit Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Test Pit Observations	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Stormwater Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Fire Alarm/Life Safety Peer Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$5,095,000	\$0	\$5,095,000	\$4,945,000	\$291,287	\$4,653,713	\$150,000		\$150,000	\$5,095,000	\$0
0201 0000 Basic Services (SMMA)											
0201 0100 Feasibility/Schematic Design	\$819,000	\$0	\$819,000	\$819,000	\$245,700	\$573,300	\$0	30%	\$0	\$819,000	\$0
0201 0400 Design Development	\$819,000	\$0	\$819,000	\$819,000	\$0	\$819,000	\$0	0%	\$0	\$819,000	\$0
0201 0500 Construction Contract Documents	\$1,228,500	\$0	\$1,228,500	\$1,228,500	\$0	\$1,228,500	\$0	0%	\$0	\$1,228,500	\$0
0201 0600 Bidding	\$204,750	\$0	\$204,750	\$204,750	\$0	\$204,750	\$0	0%	\$0	\$204,750	\$0
0201 0700 Construction Contract Administration	\$1,023,750	\$0	\$1,023,750	\$1,023,750	\$0	\$1,023,750	\$0	0%	\$0	\$1,023,750	\$0
0201 0800 Closeout	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0201 9900 Other Basic Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 0000 Reimbursable and Other Services											
0203 0200 Printing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Other Reimbursable Costs	\$50,000	\$0	\$50,000	\$50,000	\$0	\$50,000	\$0	0%	\$0	\$50,000	\$0
0203 9900 Other Misc. Reimbursable Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Permitting	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Soil Testing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Hydrant Flow Test	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Con-Com	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Stormwater	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Noise Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 FF&E/Technology Design	\$300,000	\$0	\$300,000	\$150,000	\$0	\$150,000	\$150,000	0%	\$150,000	\$300,000	\$0
0204 0000 Sub-Consultants											
0204 0200 Hazardous Materials	\$225,000	\$0	\$225,000	\$225,000	\$0	\$225,000	\$0	0%	\$0	\$225,000	\$0
0204 0300 GeoTechnical & Geo-Environmental (H&A)	\$300,000	\$0	\$300,000	\$300,000	\$24,970	\$275,030	\$0	8%	\$0	\$300,000	\$0
0204 0400 Site Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0400 Site Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0500 Wetlands	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 1200 Traffic Studies (BSC)	\$125,000	\$0	\$125,000	\$125,000	\$20,617	\$104,383	\$0	16%	\$0	\$125,000	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0301 0000 Land/Building Purchase	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0302 0000 Appraisal Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0303 0000 Recording Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$58,196,935	\$0	\$58,196,935	\$0	\$0	\$0	\$58,196,935		\$58,196,935	\$58,196,935	\$0
0501 0000 Pre-Construction Services	\$275,000	\$0	\$275,000	\$0	\$0	\$0	\$275,000		\$275,000	\$275,000	\$0
0502 0000 Construction											
0502 0000 Construction Budget	\$37,789,750	\$0	\$37,789,750	\$0	\$0	\$0	\$37,789,750		\$37,789,750	\$37,789,750	\$0
0502 0010 GMP - Fee	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0020 GMP - Insurances	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0030 CM Contingency	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100 Division 1 - General Conditions	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100 Division 1 - General Requirements	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0200 Division 2 - Existing Conditions											
0502 0200 Demolition/Abatement	\$1,590,400	\$0	\$1,590,400	\$0	\$0	\$0	\$1,590,400		\$1,590,400	\$1,590,400	\$0
0502 0300 Division 3 - Concrete	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0400 Division 4 - Masonry	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0500 Division 5 - Metals											
0502 0500 Structural Steel	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0500 Misc. Metals	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0600 Division 6 - Wood, Plastics and Composites (Finish Carpentry)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0

Manchester School District - Beech Street Elementary School Project

Manchester School District - Beech Street Elementary School Project
Project Director / Manager: David Saindon / Hamdi Cobanoglu

Period Ending
Invoice Summary Package
Includes GC/CM Requisition

5/31/2024
4
N/A

Current Budget



			Original Budget	Budget Changes	Current Budget	Committed Costs	Expended	Unspent	Remaining Budget	% Complete	CTC	Anticipated	Variance
			(A)	(B)	(C)	(D)	(E)	(F)=(D)-(E)	(G)=(C)-(D)	(against commit't g.)	(Beyond committed)	C @ C	(Under) / Over
										(H)=(E)/(J)	(I)	(J)=(D)+(I)	(K)=(C)-(J)
0502	0700	Division 7 - Thermal and Moisture Protection							\$0				
		Metal Panels	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Roofing	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Waterproofing & Dampproofing	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	0800	Division 8 - Openings							\$0				
		Metal Windows	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Hollow Metal Doors, Frames, Hardware	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Special Doors	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Glass & Glazing	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	0900	Division 9 - Finishes							\$0				
		Metal Studs and Drywall	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Tiling	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Acoustical Ceilings	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Wood Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Carpet/Resilient Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Resinous Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Painting	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	1000	Division 10 - Specialties	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Signage	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	1100	Division 11 - Equipment							\$0				
		Stage Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Food Service Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	1200	Athletic Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Division 12 - Furnishings							\$0				
		Window Treatments	\$0	\$0	\$0	\$0	\$0	\$0	\$0			\$0	\$0
0502	1400	Division 14 - Conveying Systems (Elevators)	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	2100	Division 21 - Fire Suppression	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	2200	Division 22 - Plumbing	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	2300	Division 23 - HVAC	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	2600	Division 26 - Electrical	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	3100	Division 31 - Earthwork	\$10,986,750	\$0	\$10,986,750	\$0	\$0	\$0	\$10,986,750		\$10,986,750	\$10,986,750	\$0
0502	3200	Division 32 - Exterior Improvements (Carried in Earthwork)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	9900	Retainage	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0506	0000	Alternates	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0508	0000	Change Orders	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0509	0000	Design/Pricing Contingency	\$7,555,035	\$0	\$7,555,035	\$0	\$0	\$0	\$7,555,035		\$7,555,035	\$7,555,035	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS			\$450,000	\$0	\$450,000	\$0	\$0	\$0	\$450,000		\$450,000	\$450,000	\$0
0601	0000	Utility Company Fees	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0602	0000	Testing Services	\$150,000	\$0	\$150,000	\$0	\$0	\$0	\$150,000		\$150,000	\$150,000	\$0
0603	0000	Swing Space/Modulars	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0699	0000	Other Project Costs (Moving, etc.)	\$200,000	\$0	\$200,000	\$0	\$0	\$0	\$200,000		\$200,000	\$200,000	\$0
0699	0000	Stipend for Teacher Move	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0700 0000 FURNISHINGS & EQUIPMENT			\$2,348,800	\$0	\$2,348,800	\$0	\$0	\$0	\$2,348,800		\$2,348,800	\$2,348,800	\$0
0701	0000	Furnishings & Equipment (FF+E)	\$1,174,400	\$0	\$1,174,400	\$0	\$0	\$0	\$1,174,400		\$1,174,400	\$1,174,400	\$0
0702	0000	Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0703	0000	Technology	\$1,174,400	\$0	\$1,174,400	\$0	\$0	\$0	\$1,174,400		\$1,174,400	\$1,174,400	\$0
0799	0000	Other Furnishings & Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0800 0000 OWNER'S CONTINGENCY			\$5,963,970	(\$250,000)	\$5,713,970	\$0	\$0	\$0	\$5,713,970		\$5,713,970	\$5,713,970	\$0
0801	0000	Owner's Contingency (soft)	\$828,084	(\$250,000)	\$578,084	\$0	\$0	\$0	\$578,084		\$578,084	\$578,084	\$0
0507	0000	Owner's Construction Contingency (hard)	\$5,135,886	\$0	\$5,135,886	\$0	\$0	\$0	\$5,135,886		\$5,135,886	\$5,135,886	\$0
PROJECT TOTALS			\$74,111,834	\$0	\$74,111,834	\$7,121,071	\$322,279	\$6,798,792	\$66,990,763		\$66,990,763	\$74,111,834	\$0

Manchester School District - Hillside Middle School Project



Manchester School District - Hillside Middle School Project
Project Director / Manager: David Saindon / Mark Lenfest

Period Ending 5/31/2024
Invoice Summary Package 4
Includes GC/CM Requisition N/A

Current Budget



	Original Budget [A]	Budget Changes [B]	Current Budget [C]	Committed Costs [D]	Expended [E]	Unspent [F]=[D]-[E]	Remaining Budget [G]=[C]-[D]	% Complete (against commit'd) [H]=[E]/[J]	CTC (beyond committed) [I]	Anticipated C.@ C [J]=[D]+[I]	Variance (Under) / Over [K]=[C]-[J]
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,017,155	\$0	\$1,017,155	\$976,626	\$33,340	\$943,285	\$40,529			\$1,017,155	\$0
0101 0000 Legal Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 0000 Owner's Project Manager (Leftfield)											
0102 0100 Programming/Schematic Design	\$76,728	\$0	\$76,728	\$76,728	\$33,340	\$43,387	\$0	43%	\$0	\$76,728	\$0
0102 0400 Design Development	\$57,546	\$0	\$57,546	\$57,546	\$0	\$57,546	\$0	0%	\$0	\$57,546	\$0
0102 0500 Construction Contract Docs	\$172,182	\$0	\$172,182	\$172,182	\$0	\$172,182	\$0	0%	\$0	\$172,182	\$0
0102 0600 Bidding	\$66,909	\$0	\$66,909	\$66,909	\$0	\$66,909	\$0	0%	\$0	\$66,909	\$0
0102 0700 Construction Contract Administration	\$609,254	\$0	\$609,254	\$568,725	\$0	\$568,725	\$40,529	0%	\$40,529	\$609,254	\$0
0102 0800 Closeout	\$34,537	\$0	\$34,537	\$34,537	\$0	\$34,537	\$0	0%	\$0	\$34,537	\$0
0102 0900 Extra Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1000 Reimbursable & Other Services (A&A Move Management)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1100 Cost Estimates	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 9900 Other Project Manager Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0103 0000 Advertising	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0104 0000 Permitting Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0105 0000 Owner's Insurance	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Other Administrative Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Structural Peer Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Scope of Site Plan & Special Permit Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Test Pit Observations	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Stormwater Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Fire Alarm/Life Safety Peer Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$4,087,500	\$0	\$4,087,500	\$3,937,500	\$305,743	\$3,631,757	\$150,000			\$4,087,500	\$0
0201 0000 Basic Services (SMM)											
0201 0100 Programming/Schematic Design	\$612,000	\$0	\$612,000	\$612,000	\$255,000	\$357,000	\$0	42%	\$0	\$612,000	\$0
0201 0400 Design Development	\$748,000	\$0	\$748,000	\$748,000	\$0	\$748,000	\$0	0%	\$0	\$748,000	\$0
0201 0500 Construction Contract Documents	\$1,020,000	\$0	\$1,020,000	\$1,020,000	\$0	\$1,020,000	\$0	0%	\$0	\$1,020,000	\$0
0201 0600 Bidding	\$170,000	\$0	\$170,000	\$170,000	\$0	\$170,000	\$0	0%	\$0	\$170,000	\$0
0201 0700 Construction Contract Administration	\$850,000	\$0	\$850,000	\$850,000	\$0	\$850,000	\$0	0%	\$0	\$850,000	\$0
0201 0800 Closeout	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0201 9900 Other Basic Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 0000 Reimbursable and Other Services											
0203 0200 Printing (over minimum)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Other Reimbursable Costs (consultant contingency)	\$12,500	\$0	\$12,500	\$12,500	\$0	\$12,500	\$0	0%	\$0	\$12,500	\$0
0203 9900 Other Misc. Reimbursable Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Permitting	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Soil Testing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Permitting - Transportation	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Hydrant Flow Test	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Con-Com	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Stormwater	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Noise Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 FF&E/Technology Design	\$300,000	\$0	\$300,000	\$150,000	\$0	\$150,000	\$150,000	0%	\$150,000	\$300,000	\$0
0204 0000 Sub-Consultants											
0204 0200 Hazardous Materials	\$150,000	\$0	\$150,000	\$150,000	\$0	\$150,000	\$0	0%	\$0	\$150,000	\$0
0204 0300 GeoTechnical & Geo-Environmental (H&A)	\$125,000	\$0	\$125,000	\$125,000	\$37,620	\$87,380	\$0	30%	\$0	\$125,000	\$0
0204 0400 Site Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0500 Wetlands	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 1200 Traffic Studies (BSC)	\$100,000	\$0	\$100,000	\$100,000	\$13,123	\$86,877	\$0	13%	\$0	\$100,000	\$0
0300 0000 SITE ACQUISITION IN/AI	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0301 0000 Land/Building Purchase	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0302 0000 Appraisal Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0303 0000 Recording Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$43,527,708	\$0	\$43,527,708	\$0	\$0	\$0	\$43,527,708		\$43,527,708	\$43,527,708	\$0
0501 0000 Pre-Construction Services	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0502 0000 Construction											
0502 0000 Construction Budget	\$34,063,224	\$0	\$34,063,224	\$0	\$0	\$0	\$34,063,224		\$34,063,224	\$34,063,224	\$0
0502 0010 GMP - Fee	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0020 GMP - Insurances	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0030 CM Contingency	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100 Division 1 - General Conditions	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100 Division 1 - General Requirements	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0200 Division 2 - Existing Conditions											
0502 0200 Demolition/Abatement	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0300 Division 3 - Concrete	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0400 Division 4 - Masonry	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0500 Division 5 - Metals											
0502 0500 Structural Steel	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0500 Misc. Metals	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0600 Division 6 - Wood, Plastics and Composites (Finish Carpentry)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0

Manchester School District - Hillside Middle School Project



Manchester School District - Hillside Middle School Project
Project Director / Manager: David Saindon / Mark Lenfest

Period Ending 5/31/2024
Invoice Summary Package 4
Includes GC/CM Requisition N/A

Current Budget



		Original Budget	Budget Changes	Current Budget	Committed Costs	Expended	Unspent	Remaining Budget	% Complete	CTC	Anticipated	Variance
		[A]	[B]	[C]	[D]	[E]	[F]=[D]-[E]	[G]=[C]-[D]	(against commit'd) [H]=[E]/[J]	(beyond committed) [I]	C @ C [J]=[D]+[I]	(Under) / Over [K]=[C]-[J]
0502	0700	Division 7 - Thermal and Moisture Protection						\$0				
		Metal Panels	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Roofing	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Waterproofing & Dampproofing	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	0800	Division 8 - Openings						\$0				
		Metal Windows	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Hollow Metal Doors, Frames, Hardware	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Special Doors	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Glass & Glazing	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	0900	Division 9 - Finishes						\$0				
		Metal Studs and Drywall	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Tiling	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Acoustical Ceilings	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Wood Flooring	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Carpet/Resilient Flooring	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Resinous Flooring	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Painting	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 10 - Specialties	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1000	Signage	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 11 - Equipment										
		Stage Equipment	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1100	Food Service Equipment	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Athletic Equipment	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 12 - Furnishings						\$0				
0502	1200	Window Treatments	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 14 - Conveying Systems (Elevators)	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1400	Division 21 - Fire Suppression	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2100	Division 22 - Plumbing	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2200	Division 23 - HVAC	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2300	Division 26 - Electrical	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2600	Division 31 - Earthwork	\$3,700,000	\$0	\$3,700,000	\$0	\$0	\$3,700,000		\$3,700,000	\$3,700,000	\$0
0502	3100	Division 32 - Exterior Improvements (Landscaping)	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	3200	Retainage	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	9900	Alternates	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0506	0000	Change Orders	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0508	0000	Design/Pricing Contingency	\$5,664,484	\$0	\$5,664,484	\$0	\$0	\$5,664,484		\$5,664,484	\$5,664,484	\$0
0509	0000											
0600	0000	MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$250,000		\$250,000	\$250,000	\$0
0601	0000	Utility Company Fees	\$100,000	\$0	\$100,000	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0602	0000	Testing Services	\$50,000	\$0	\$50,000	\$0	\$0	\$50,000		\$50,000	\$50,000	\$0
0603	0000	Swing Space/Modulars	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0699	0000	Other Project Costs (Moving, etc.)	\$100,000	\$0	\$100,000	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0699	0000	Stipend for Teacher Move	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0700	0000	FURNISHINGS & EQUIPMENT	\$3,520,000	\$0	\$3,520,000	\$0	\$0	\$3,520,000		\$3,520,000	\$3,520,000	\$0
0701	0000	Furnishings & Equipment (FF+E)	\$1,760,000	\$0	\$1,760,000	\$0	\$0	\$1,760,000		\$1,760,000	\$1,760,000	\$0
0702	0000	Equipment	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0703	0000	Technology	\$1,760,000	\$0	\$1,760,000	\$0	\$0	\$1,760,000		\$1,760,000	\$1,760,000	\$0
0799	0000	Other Furnishings & Equipment	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0800	0000	OWNER'S CONTINGENCY	\$4,601,489	\$0	\$4,601,489	\$0	\$0	\$4,601,489		\$4,601,489	\$4,601,489	\$0
0801	0000	Owner's Contingency (soft)	\$713,393	\$0	\$713,393	\$0	\$0	\$713,393		\$713,393	\$713,393	\$0
0507	0000	Owner's Construction Contingency (hard)	\$3,888,096	\$0	\$3,888,096	\$0	\$0	\$3,888,096		\$3,888,096	\$3,888,096	\$0
PROJECT TOTALS		\$57,003,852	\$0	\$57,003,852	\$4,914,126	\$339,083	\$4,575,042	\$52,089,726		\$52,089,726	\$57,003,852	\$0

Manchester School District - McLaughlin Middle School Project



Manchester School District - McLaughlin Middle School Project
Project Director / Manager: David Saindon / Mark Lenfest

Period Ending
Invoice Summary Package
Includes GC/CM Requisition

5/31/2024
4
N/A

Current Budget



	Original Budget (A)	Budget Changes (B)	Current Budget (C)	Committed Costs (D)	Expended (E)	Unspent (F)=(D)-(E)	Remaining Budget (G)=(C)-(D)	% Complete (against committed) (H)=(E)/(J)	CTC (beyond committed) (I)	Anticipated C @ C (J)=(D)+(I)	Variance (Under) / Over (K)=(C)-(J)
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,017,155	\$0	\$1,017,155	\$976,626	\$32,053	\$944,573	\$40,529		\$40,529	\$1,017,155	\$0
0101 0000 Legal Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 0000 Owner's Project Manager (Leftfield)											
0102 0100 Programming/Schematic Design	\$76,728	\$0	\$76,728	\$76,728	\$32,053	\$44,675	\$0	42%	\$0	\$76,728	\$0
0102 0400 Design Development	\$57,546	\$0	\$57,546	\$57,546	\$0	\$57,546	\$0	0%	\$0	\$57,546	\$0
0102 0500 Construction Contract Docs	\$172,182	\$0	\$172,182	\$172,182	\$0	\$172,182	\$0	0%	\$0	\$172,182	\$0
0102 0600 Bidding	\$66,909	\$0	\$66,909	\$66,909	\$0	\$66,909	\$0	0%	\$0	\$66,909	\$0
0102 0700 Construction Contract Administration	\$609,254	\$0	\$609,254	\$568,725	\$0	\$568,725	\$40,529	0%	\$40,529	\$609,254	\$0
0102 0800 Closeout	\$34,537	\$0	\$34,537	\$34,537	\$0	\$34,537	\$0	0%	\$0	\$34,537	\$0
0102 0900 Extra Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1000 Reimbursable & Other Services (A&A Move Management)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1100 Cost Estimates	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 9900 Other Project Manager Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0103 0000 Advertising	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0104 0000 Permitting Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0105 0000 Owner's Insurance	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Other Administrative Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Structural Peer Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Scope of Site Plan & Special Permit Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Test Pit Observations	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Stormwater Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Fire Alarm/Life Safety Peer Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$3,232,500	\$0	\$3,232,500	\$3,082,500	\$243,473	\$2,839,027	\$150,000		\$150,000	\$3,232,500	\$0
0201 0000 Basic Services (SMMA)											
0201 0100 Programming/Schematic Design	\$468,000	\$0	\$468,000	\$468,000	\$195,000	\$273,000	\$0	42%	\$0	\$468,000	\$0
0201 0400 Design Development	\$572,000	\$0	\$572,000	\$572,000	\$0	\$572,000	\$0	0%	\$0	\$572,000	\$0
0201 0500 Construction Contract Documents	\$780,000	\$0	\$780,000	\$780,000	\$0	\$780,000	\$0	0%	\$0	\$780,000	\$0
0201 0600 Bidding	\$130,000	\$0	\$130,000	\$130,000	\$0	\$130,000	\$0	0%	\$0	\$130,000	\$0
0201 0700 Construction Contract Administration	\$650,000	\$0	\$650,000	\$650,000	\$0	\$650,000	\$0	0%	\$0	\$650,000	\$0
0201 0800 Closeout	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0201 9900 Other Basic Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 0000 Reimbursable and Other Services											
0203 0200 Printing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Other Reimbursable Costs	\$12,500	\$0	\$12,500	\$12,500	\$0	\$12,500	\$0	0%	\$0	\$12,500	\$0
0203 9900 Other Misc. Reimbursable Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Permitting	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Soil Testing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Permitting	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Hydrant Flow Test	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Con-Com	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Stormwater	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Noise Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 FF&E/Technology Design	\$300,000	\$0	\$300,000	\$150,000	\$0	\$150,000	\$150,000	0%	\$150,000	\$300,000	\$0
0204 0000 Sub-Consultants											
0204 0200 Hazardous Materials	\$100,000	\$0	\$100,000	\$100,000	\$0	\$100,000	\$0	0%	\$0	\$100,000	\$0
0204 0300 GeoTechnical & Geo-Environmental (H&A)	\$120,000	\$0	\$120,000	\$120,000	\$33,220	\$86,780	\$0	28%	\$0	\$120,000	\$0
0204 0400 Site Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0500 Wetlands	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 1200 Traffic Studies (BSC)	\$100,000	\$0	\$100,000	\$100,000	\$15,253	\$84,747	\$0	15%	\$0	\$100,000	\$0
0300 0000 SITE ACQUISITION IN/A	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0301 0000 Land/Building Purchase	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0302 0000 Appraisal Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0303 0000 Recording Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$28,827,403	\$0	\$28,827,403	\$0	\$0	\$0	\$28,827,403		\$28,827,403	\$28,827,403	\$0
0501 0000 Pre-Construction Services	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0502 0000 Construction											
0502 0000 Construction Budget	\$20,080,350	\$0	\$20,080,350	\$0	\$0	\$0	\$20,080,350		\$20,080,350	\$20,080,350	\$0
0502 0010 GMP - Fee	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0020 GMP - Insurances	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0030 CM Contingency	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100 Division 1 - General Conditions	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100 Division 1 - General Requirements	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0200 Division 2 - Existing Conditions											
0502 0200 Demolition/Abatement	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0300 Division 3 - Concrete	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0400 Division 4 - Masonry	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0500 Division 5 - Metals											
0502 0500 Structural Steel	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0500 Misc. Metals	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0600 Division 6 - Wood, Plastics and Composites (Finish Carpentry)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0

Manchester School District - McLaughlin Middle School Project



Manchester School District - McLaughlin Middle School Project
Project Director / Manager: David Saindon / Mark Lenfest

Period Ending
Invoice Summary Package
Includes GC/CM Requisition

5/31/2024
4
N/A

Current Budget



		Original Budget [A]	Budget Changes [B]	Current Budget [C]	Committed Costs [D]	Expended [E]	Unspent [F]=[D]-[E]	Remaining Budget [G]=[C]-[D]	% Complete (against commit'd) [H]=[E]/[J]	CTC (beyond committed) [I]	Anticipated C @ C [J]=[D]+[I]	Variance (Under) / Over [K]=[C]-[J]
	Division 7 - Thermal and Moisture Protection											
0502	0700											
	Metal Panels	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Roofing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Waterproofing & Dampproofing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Division 8 - Openings											
0502	0800											
	Metal Windows	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Hollow Metal Doors, Frames, Hardware	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Special Doors	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Glass & Glazing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Division 9 - Finishes											
0502	0900											
	Metal Studs and Drywall	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Tiling	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Acoustical Ceilings	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Wood Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Carpet/Resilient Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Resinous Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Painting	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1000											
	Division 10 - Specialties	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Signage	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Division 11 - Equipment											
0502	1100											
	Stage Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Food Service Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Athletic Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1200											
	Division 12 - Furnishings											
	Window Treatments	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1400											
	Division 14 - Conveying Systems (Elevators)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2100											
	Division 21 - Fire Suppression	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2200											
	Division 22 - Plumbing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2300											
	Division 23 - HVAC	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2600											
	Division 26 - Electrical	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	3100											
	Division 31 - Earthwork	\$4,900,000	\$0	\$4,900,000	\$0	\$0	\$0	\$4,900,000		\$4,900,000	\$4,900,000	\$0
0502	3200											
	Division 32 - Exterior Improvements (Landscaping)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	9900											
	Retainage	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0506	0000											
	Alternates	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0508	0000											
	Change Orders	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0509	0000											
	Design/Pricing Contingency	\$3,747,053	\$0	\$3,747,053	\$0	\$0	\$0	\$3,747,053		\$3,747,053	\$3,747,053	\$0
0600	0000											
	MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$0	\$250,000		\$250,000	\$250,000	\$0
0601	0000											
	Utility Company Fees	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0602	0000											
	Testing Services	\$50,000	\$0	\$50,000	\$0	\$0	\$0	\$50,000		\$50,000	\$50,000	\$0
0603	0000											
	Swing Space/Modulars	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0699	0000											
	Other Project Costs (Moving, etc.)	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0699	0000											
	Stipend for Teacher Move	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0700	0000											
	FURNISHINGS & EQUIPMENT	\$3,200,000	\$0	\$3,200,000	\$0	\$0	\$0	\$3,200,000		\$3,200,000	\$3,200,000	\$0
0701	0000											
	Furnishings & Equipment (FF+E)	\$1,600,000	\$0	\$1,600,000	\$0	\$0	\$0	\$1,600,000		\$1,600,000	\$1,600,000	\$0
0702	0000											
	Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0703	0000											
	Technology	\$1,600,000	\$0	\$1,600,000	\$0	\$0	\$0	\$1,600,000		\$1,600,000	\$1,600,000	\$0
0799	0000											
	Other Furnishings & Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0800	0000											
	OWNER'S CONTINGENCY	\$3,161,130	\$0	\$3,161,130	\$0	\$0	\$0	\$3,161,130		\$3,161,130	\$3,161,130	\$0
0801	0000											
	Owner's Contingency (soft)	\$507,181	\$0	\$507,181	\$0	\$0	\$0	\$507,181		\$507,181	\$507,181	\$0
0507	0000											
	Owner's Construction Contingency (hard)	\$2,653,949	\$0	\$2,653,949	\$0	\$0	\$0	\$2,653,949		\$2,653,949	\$2,653,949	\$0
PROJECT TOTALS		\$39,688,188	\$0	\$39,688,188	\$4,059,126	\$275,526	\$3,783,600	\$35,629,062		\$35,629,062	\$39,688,188	\$0

Manchester School District - Southside Middle School Project



Manchester School District - Southside Middle School Project
Project Director / Manager: David Saindon / Linda Liporto

Period Ending 5/31/2024
Invoice Summary Package 4
Includes GC/CM Requisition N/A

Current Budget



	Original Budget [A]	Budget Changes [B]	Current Budget [C]	Committed Costs [D]	Expended [E]	Unspent [F]=[D]-[E]	Remaining Budget [G]=[C]-[D]	% Complete (against committed) [H]=[E]/[J]	CTC (beyond committed) [I]	Anticipated C.@C [J]=[D]+[I]	Variance (Under) / Over [K]=[C]-[J]
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,101,287	\$0	\$1,101,287	\$1,057,381	\$33,450	\$1,023,930	\$43,907		\$43,907	\$1,101,287	\$0
0101 0000 Legal Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 0000 Owner's Project Manager (Leftfield)											
0102 0100 Programming/Schematic Design	\$72,469	\$0	\$72,469	\$69,091	\$33,450	\$35,641	\$3,378	48%	\$3,378	\$72,469	\$0
0102 0400 Design Development	\$57,546	\$0	\$57,546	\$57,546	\$0	\$57,546	\$0	0%	\$0	\$57,546	\$0
0102 0500 Construction Contract Docs	\$115,092	\$0	\$115,092	\$115,092	\$0	\$115,092	\$0	0%	\$0	\$115,092	\$0
0102 0600 Bidding	\$52,637	\$0	\$52,637	\$52,637	\$0	\$52,637	\$0	0%	\$0	\$52,637	\$0
0102 0700 Construction Contract Administration	\$763,016	\$0	\$763,016	\$735,997	\$0	\$735,997	\$27,019	0%	\$27,019	\$763,016	\$0
0102 0800 Closeout	\$40,529	\$0	\$40,529	\$27,019	\$0	\$27,019	\$13,510	0%	\$13,510	\$40,529	\$0
0102 0900 Extra Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1000 Reimbursable & Other Services (A&A Move Management)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1100 Cost Estimates	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 9900 Other Project Manager Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0103 0000 Advertising	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0104 0000 Permitting Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0105 0000 Owner's Insurance	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Other Administrative Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Structural Peer Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Scope of Site Plan & Special Permit Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Test Pit Observations	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Stormwater Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Fire Alarm/Life Safety Peer Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$4,317,500	\$0	\$4,317,500	\$4,167,500	\$43,200	\$4,124,300	\$150,000		\$150,000	\$4,317,500	\$0
0201 0000 Basic Services (SMM)											
0201 0100 Programming/Schematic Design	\$648,000	\$0	\$648,000	\$648,000	\$43,200	\$604,800	\$0	7%	\$0	\$648,000	\$0
0201 0400 Design Development	\$792,000	\$0	\$792,000	\$792,000	\$0	\$792,000	\$0	0%	\$0	\$792,000	\$0
0201 0500 Construction Contract Documents	\$1,080,000	\$0	\$1,080,000	\$1,080,000	\$0	\$1,080,000	\$0	0%	\$0	\$1,080,000	\$0
0201 0600 Bidding	\$180,000	\$0	\$180,000	\$180,000	\$0	\$180,000	\$0	0%	\$0	\$180,000	\$0
0201 0700 Construction Contract Administration	\$900,000	\$0	\$900,000	\$900,000	\$0	\$900,000	\$0	0%	\$0	\$900,000	\$0
0201 0800 Closeout	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0201 9900 Other Basic Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 0000 Reimbursable and Other Services											
0203 0200 Printing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Other Reimbursable Costs	\$12,500	\$0	\$12,500	\$12,500	\$0	\$12,500	\$0	0%	\$0	\$12,500	\$0
0203 9900 Other Misc. Reimbursable Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Permitting	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Soil Testing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Hydrant Flow Test	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Con-Com	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Stormwater	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Noise Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 FF&E/Technology Design	\$300,000	\$0	\$300,000	\$150,000	\$0	\$150,000	\$150,000	0%	\$150,000	\$300,000	\$0
0204 0000 Sub-Consultants											
0204 0200 Hazardous Materials	\$175,000	\$0	\$175,000	\$175,000	\$0	\$175,000	\$0	0%	\$0	\$175,000	\$0
0204 0300 GeoTechnical & Geo-Environmental	\$130,000	\$0	\$130,000	\$130,000	\$0	\$130,000	\$0	0%	\$0	\$130,000	\$0
0204 0400 Site Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0500 Wetlands	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 1200 Traffic Studies	\$100,000	\$0	\$100,000	\$100,000	\$0	\$100,000	\$0	0%	\$0	\$100,000	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0301 0000 Land/Building Purchase	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0302 0000 Appraisal Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0303 0000 Recording Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$46,685,769	\$0	\$46,685,769	\$0	\$0	\$0	\$46,685,769		\$46,685,769	\$46,685,769	\$0
0501 0000 Pre-Construction Services	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0502 0000 Construction											
0502 0000 Construction Budget	\$35,121,474	\$0	\$35,121,474	\$0	\$0	\$0	\$35,121,474		\$35,121,474	\$35,121,474	\$0
0502 0010 GMP - Fee	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0020 GMP - Insurances	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0030 CM Contingency	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100 Division 1 - General Conditions	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100 Division 1 - General Requirements	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0200 Division 2 - Existing Conditions											
0502 0200 Demolition/Abatement	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0300 Division 3 - Concrete	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0400 Division 4 - Masonry	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0500 Division 5 - Metals											
0502 0500 Structural Steel	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0500 Misc. Metals	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0600 Division 6 - Wood, Plastics and Composites (Finish Carpentry)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0600 Division 7 - Thermal and Moisture Protection							\$0				

Manchester School District - Southside Middle School Project



Manchester School District - Southside Middle School Project
Project Director / Manager: David Saindon / Linda Liporto

Period Ending 5/31/2024
Invoice Summary Package 4
Includes GC/CM Requisition N/A

Current Budget



			Original Budget	Budget Changes	Current Budget	Committed Costs	Expended	Unspent	Remaining Budget	% Complete	CTC	Anticipated	Variance
			[A]	[B]	[C]	[D]	[E]	[F]=[D]-[E]	[G]=[C]-[D]	(against commit'd) [H]=[E]/[J]	(beyond committed) [I]	C @ C [J]=[D]+[I]	(Under) / Over [K]=[C]-[J]
0502	0700	Metal Panels	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Roofing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Waterproofing & Dampproofing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 8 - Openings							\$0				
		Metal Windows	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	0800	Hollow Metal Doors, Frames, Hardware	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Special Doors	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Glass & Glazing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 9 - Finishes							\$0				
		Metal Studs and Drywall	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Tiling	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	0900	Acoustical Ceilings	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Wood Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Carpet/Resilient Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Resinous Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Painting	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1000	Division 10 - Specialties	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Signage	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 11 - Equipment											
0502	1100	Stage Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Food Service Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Athletic Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1200	Division 12 - Furnishings							\$0				
		Window Treatments	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1400	Division 14 - Conveying Systems (Elevators)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2100	Division 21 - Fire Suppression	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2200	Division 22 - Plumbing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2300	Division 23 - HVAC	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2600	Division 26 - Electrical	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	3100	Division 31 - Earthwork	\$3,700,000	\$0	\$3,700,000	\$0	\$0	\$0	\$3,700,000		\$3,700,000	\$3,700,000	\$0
0502	3200	Division 32 - Exterior Improvements (Landscaping)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	9900	Retainage	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0506	0000	Alternates	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0508	0000	Change Orders	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0509	0000	Design/Pricing Contingency	\$7,764,295	\$0	\$7,764,295	\$0	\$0	\$0	\$7,764,295		\$7,764,295	\$7,764,295	\$0
0600	0000	MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$0	\$250,000		\$250,000	\$250,000	\$0
0601	0000	Utility Company Fees	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0602	0000	Testing Services	\$50,000	\$0	\$50,000	\$0	\$0	\$0	\$50,000		\$50,000	\$50,000	\$0
0603	0000	Swing Space/Modulars	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0699	0000	Other Project Costs (Moving, etc.)	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0699	0000	Stipend for Teacher Move	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0700	0000	FURNISHINGS & EQUIPMENT	\$3,200,000	\$0	\$3,200,000	\$0	\$0	\$0	\$3,200,000		\$3,200,000	\$3,200,000	\$0
0701	0000	Furnishings & Equipment (FF+E)	\$1,600,000	\$0	\$1,600,000	\$0	\$0	\$0	\$1,600,000		\$1,600,000	\$1,600,000	\$0
0702	0000	Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0703	0000	Technology	\$1,600,000	\$0	\$1,600,000	\$0	\$0	\$0	\$1,600,000		\$1,600,000	\$1,600,000	\$0
0799	0000	Other Furnishings & Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0800	0000	OWNER'S CONTINGENCY	\$4,897,135	\$0	\$4,897,135	\$0	\$0	\$0	\$4,897,135		\$4,897,135	\$4,897,135	\$0
0801	0000	Owner's Contingency (soft)	\$752,980	\$0	\$752,980	\$0	\$0	\$0	\$752,980		\$752,980	\$752,980	\$0
0507	0000	Owner's Construction Contingency (hard)	\$4,144,155	\$0	\$4,144,155	\$0	\$0	\$0	\$4,144,155		\$4,144,155	\$4,144,155	\$0
PROJECT TOTALS			\$60,451,691	\$0	\$60,451,691	\$5,224,881	\$76,650	\$5,148,230	\$55,226,811		\$55,226,811	\$60,451,691	\$0

Manchester School District - Parkside Middle School Project



Manchester School District - Parkside Middle School Project
Project Director / Manager: David Saindon / Linda Liporto

Period Ending 5/31/2024
Invoice Summary Package 4
Includes GC/CM Requisition N/A

Current Budget



	Original Budget [A]	Budget Changes [B]	Current Budget [C]	Committed Costs [D]	Expended [E]	Unspent [F]=[D]-[E]	Remaining Budget [G]=[C]-[D]	% Complete (against committd) [H]=[E]/[J]	CTC (beyond committed) [I]	Anticipated C @ C [J]=[D]+[I]	Variance (Under) / Over [K]=[C]-[J]
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,101,287	\$0	\$1,101,287	\$1,057,381	\$35,663	\$1,021,718	\$43,907		\$43,907	\$1,101,287	\$0
0101 0000 Legal Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 0000 Owner's Project Manager (Leftfield)											
0102 0100 Programming/Schematic Design	\$72,469	\$0	\$72,469	\$69,091	\$35,663	\$33,428	\$3,378	52%	\$3,378	\$72,469	\$0
0102 0400 Design Development	\$57,546	\$0	\$57,546	\$57,546	\$0	\$57,546	\$0	0%	\$0	\$57,546	\$0
0102 0500 Construction Contract Docs	\$115,092	\$0	\$115,092	\$115,092	\$0	\$115,092	\$0	0%	\$0	\$115,092	\$0
0102 0600 Bidding	\$52,637	\$0	\$52,637	\$52,637	\$0	\$52,637	\$0	0%	\$0	\$52,637	\$0
0102 0700 Construction Contract Administration	\$763,016	\$0	\$763,016	\$735,997	\$0	\$735,997	\$27,019	0%	\$27,019	\$763,016	\$0
0102 0800 Closeout	\$40,529	\$0	\$40,529	\$27,019	\$0	\$27,019	\$13,510	0%	\$13,510	\$40,529	\$0
0102 0900 Extra Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1000 Reimbursable & Other Services (A&A Move Management)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1100 Cost Estimates	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 9900 Other Project Manager Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0103 0000 Advertising	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0104 0000 Permitting Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0105 0000 Owner's Insurance	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Other Administrative Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Structural Peer Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Scope of Site Plan & Special Permit Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Test Pit Observations	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Stormwater Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Fire Alarm/Life Safety Peer Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$3,927,500	\$0	\$3,927,500	\$3,777,500	\$38,400	\$3,739,100	\$150,000		\$150,000	\$3,927,500	\$0
0201 0000 Basic Services											
0201 0100 Programming/Schematic Design	\$576,000	\$0	\$576,000	\$576,000	\$38,400	\$537,600	\$0	7%	\$0	\$576,000	\$0
0201 0400 Design Development	\$704,000	\$0	\$704,000	\$704,000	\$0	\$704,000	\$0	0%	\$0	\$704,000	\$0
0201 0500 Construction Contract Documents	\$960,000	\$0	\$960,000	\$960,000	\$0	\$960,000	\$0	0%	\$0	\$960,000	\$0
0201 0600 Bidding	\$160,000	\$0	\$160,000	\$160,000	\$0	\$160,000	\$0	0%	\$0	\$160,000	\$0
0201 0700 Construction Contract Administration	\$800,000	\$0	\$800,000	\$800,000	\$0	\$800,000	\$0	0%	\$0	\$800,000	\$0
0201 0800 Closeout	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0201 9900 Other Basic Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 0000 Reimbursable and Other Services											
0203 0200 Printing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Other Reimbursable Costs	\$12,500	\$0	\$12,500	\$12,500	\$0	\$12,500	\$0	0%	\$0	\$12,500	\$0
0203 9900 Other Misc. Reimbursable Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Permitting	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Soil Testing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Hydrant Flow Test	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Permitting	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Con-Com	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Stormwater	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Noise Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 FF&E/Technology Design	\$300,000	\$0	\$300,000	\$150,000	\$0	\$150,000	\$150,000	0%	\$150,000	\$300,000	\$0
0204 0000 Sub-Consultants											
0204 0200 Hazardous Materials	\$175,000	\$0	\$175,000	\$175,000	\$0	\$175,000	\$0	0%	\$0	\$175,000	\$0
0204 0300 GeoTechnical & Geo-Environmental	\$140,000	\$0	\$140,000	\$140,000	\$0	\$140,000	\$0	0%	\$0	\$140,000	\$0
0204 0400 Site Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0500 Wetlands	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 1200 Traffic Studies	\$100,000	\$0	\$100,000	\$100,000	\$0	\$100,000	\$0	0%	\$0	\$100,000	\$0
0300 0000 SITE ACQUISITION [NA]	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0301 0000 Land/Building Purchase	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0302 0000 Appraisal Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0303 0000 Recording Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$36,146,140	\$0	\$36,146,140	\$0	\$0	\$0	\$36,146,140		\$36,146,140	\$36,146,140	\$0
0501 0000 Pre-Construction Services	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0502 0000 Construction											
0502 0000 Construction Budget	\$24,538,450	\$0	\$24,538,450	\$0	\$0	\$0	\$24,538,450		\$24,538,450	\$24,538,450	\$0
0502 0010 GMP - Fee	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0020 GMP - Insurances	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0030 CM Contingency	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100 Division 1 - General Conditions	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100 Division 1 - General Requirements	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0200 Division 2 - Existing Conditions											
0502 0200 Demolition/Abatement	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0300 Division 3 - Concrete	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0400 Division 4 - Masonry	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0500 Division 5 - Metals											
0502 0500 Structural Steel	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0500 Misc. Metals	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0600 Division 6 - Wood, Plastics and Composites (Finish Carpentry)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0

Manchester School District - Parkside Middle School Project



Manchester School District - Parkside Middle School Project
Project Director / Manager: David Saindon / Linda Lipotto

Period Ending 5/31/2024
Invoice Summary Package 4
Includes GC/CM Requisition N/A

Current Budget



		Original Budget	Budget Changes	Current Budget	Committed Costs	Expended	Unspent	Remaining Budget	% Complete	CTC	Anticipated	Variance
		[A]	[B]	[C]	[D]	[E]	[F]=[D]-[E]	[G]=[C]-[D]	(against commit'd) [H]=[E]/[J]	(beyond committed) [I]	C @ C [J]=[D]+[I]	(Under) / Over [K]=[C]-[J]
0502	0700	Division 7 - Thermal and Moisture Protection						\$0				
		Metal Panels	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Roofing	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Waterproofing & Dampproofing	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	0800	Division 8 - Openings						\$0				
		Metal Windows	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Hollow Metal Doors, Frames, Hardware	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Special Doors	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Glass & Glazing	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	0900	Division 9 - Finishes						\$0				
		Metal Studs and Drywall	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Tiling	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Acoustical Ceilings	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Wood Flooring	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Carpet/Resilient Flooring	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Resinous Flooring	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Painting	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 10 - Specialties	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1000	Signage	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 11 - Equipment										
		Stage Equipment	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1100	Food Service Equipment	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Athletic Equipment	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 12 - Furnishings						\$0				
0502	1200	Window Treatments	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 14 - Conveying Systems (Elevators)	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1400	Division 21 - Fire Suppression	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2100	Division 22 - Plumbing	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2200	Division 23 - HVAC	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2300	Division 26 - Electrical	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2600	Division 31 - Earthwork	\$5,500,000	\$0	\$5,500,000	\$0	\$0	\$5,500,000		\$5,500,000	\$5,500,000	\$0
0502	3100	Division 32 - Exterior Improvements (Landscaping)	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	3200	Retainage	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	9900	Alternates	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0506	0000	Change Orders	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0508	0000	Design/Pricing Contingency	\$6,007,690	\$0	\$6,007,690	\$0	\$0	\$6,007,690		\$6,007,690	\$6,007,690	\$0
0509	0000											
0600	0000	MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$250,000		\$250,000	\$250,000	\$0
0601	0000	Utility Company Fees	\$100,000	\$0	\$100,000	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0602	0000	Testing Services	\$50,000	\$0	\$50,000	\$0	\$0	\$50,000		\$50,000	\$50,000	\$0
0603	0000	Swing Space/Modulars	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0699	0000	Other Project Costs (Moving, etc.)	\$100,000	\$0	\$100,000	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0699	0000	Stipend for Teacher Move	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0700	0000	FURNISHINGS & EQUIPMENT	\$3,200,000	\$0	\$3,200,000	\$0	\$0	\$3,200,000		\$3,200,000	\$3,200,000	\$0
0701	0000	Furnishings & Equipment (FF+E)	\$1,600,000	\$0	\$1,600,000	\$0	\$0	\$1,600,000		\$1,600,000	\$1,600,000	\$0
0702	0000	Equipment	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0703	0000	Technology	\$1,600,000	\$0	\$1,600,000	\$0	\$0	\$1,600,000		\$1,600,000	\$1,600,000	\$0
0799	0000	Other Furnishings & Equipment	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0800	0000	OWNER'S CONTINGENCY	\$3,877,019	\$0	\$3,877,019	\$0	\$0	\$3,877,019		\$3,877,019	\$3,877,019	\$0
0801	0000	Owner's Contingency (soft)	\$608,899	\$0	\$608,899	\$0	\$0	\$608,899		\$608,899	\$608,899	\$0
0507	0000	Owner's Construction Contingency (hard)	\$3,268,120	\$0	\$3,268,120	\$0	\$0	\$3,268,120		\$3,268,120	\$3,268,120	\$0
PROJECT TOTALS		\$48,501,946	\$0	\$48,501,946	\$4,834,881	\$74,063	\$4,760,818	\$43,667,066		\$43,667,066	\$48,501,946	\$0

ATTACHMENT B

Invoice Log For Reporting Period

Manchester Priority One Projects**Modular/Beech St. ES/Hillside MS/McLaughlin MS/Parkside MS/Southside MS - Invoice Approval Summary****Date** 6/4/2024**Period Ending:** 5/31/2024**Leftfield Invoice Summary #:** 4

Project	Invoice #	Invoice Date	Contractor/Vendor	Amount
Modular	App #5	5/31/2024	Triumph Modular - May 2024 Modular Services	\$888,241.29
Total to Pay to Triumph Modular:				\$888,241.29
Modular	3	5/31/2024	Leftfield - Modular - May 2024 OPM Services	\$33,579.10
Modular [FFE + Tech]	3	5/31/2024	Leftfield - Modular [FFE + Tech] - May 2024 OPM Services	\$376.25
Beech	3	5/31/2024	Leftfield - Beech - May 2024 OPM Services	\$9,943.35
Hillside	3	5/31/2024	Leftfield - Hillside - May 2024 OPM Services	\$9,947.85
McLaughlin	3	5/31/2024	Leftfield - McLaughlin - May 2024 OPM Services	\$11,680.35
Parkside	3	5/31/2024	Leftfield - Parkside - May 2024 OPM Services	\$10,802.85
Southside	3	5/31/2024	Leftfield - Southside - May 2024 OPM Services	\$10,720.35
Total to Pay to Leftfield:				\$87,050.10
Modular	61339	5/30/2024	SMMA - Modular - Construction	\$40,800.00
Modular	61339	5/30/2024	SMMA - Modular - BSC Group - Survey Consultant Costs	\$57,287.03
McLaughlin	61341	5/30/2024	SMMA - McLaughlin - Programming	\$3,900.00
McLaughlin	61341	5/30/2024	SMMA - McLaughlin - Schematic Design	\$58,500.00
McLaughlin	61341	5/30/2024	SMMA - McLaughlin - BSC Group - Traffic Consulting	\$7,626.30
Hillside	61342	5/30/2024	SMMA - Hillside - Programming	\$10,200.00
Hillside	61342	5/30/2024	SMMA - Hillside - Schematic Design	\$76,500.00
Hillside	61342	5/30/2024	SMMA - Hillside - BSC Group - Traffic Consulting	\$7,873.80
Beech	61340	5/30/2024	SMMA - Beech - Feasibility	\$131,040.00
Beech	61340	5/30/2024	SMMA - Beech - BSC Group - Traffic Consulting	\$14,173.94
Parkside	61343	5/30/2024	SMMA - Parkside - Programming	\$19,200.00
Southside	61344	5/30/2024	SMMA - Southside - Programming	\$21,600.00
Total to Pay to SMMA :				\$448,701.07
Modular	Req #1	5/31/2024	Consigli Construction - Modular - May 2024	\$1,185,343.51
Total to Pay to Consigli Construction :				\$1,185,343.51

Subtotal Modular Invoices	\$2,205,627.18
Subtotal Hillside Middle School Invoices	\$104,521.65
Subtotal McLaughlin Middle School Invoices	\$81,706.65
Subtotal Parkside Middle School Invoices	\$30,002.85
Subtotal Beech Street Invoices	\$155,157.29
Subtotal Southside Middle School Invoices	\$32,320.35
Total of Invoices Submitted	\$2,609,335.97



6 / 4 / 24

Recommended by Leftfield Project Manager

Date

Approved by Dr. Jennifer Gillis, Superintendent of Schools

Date

Approved by Ms. Karen DeFrancis, Chief Financial Officer


Date

ATTACHMENT C

Priority One Schedule Rolled-Up
Individual Project Schedules – Detail

PRIORITY 1 PROJECT SCHEDULE


06-Jun-24 18:11

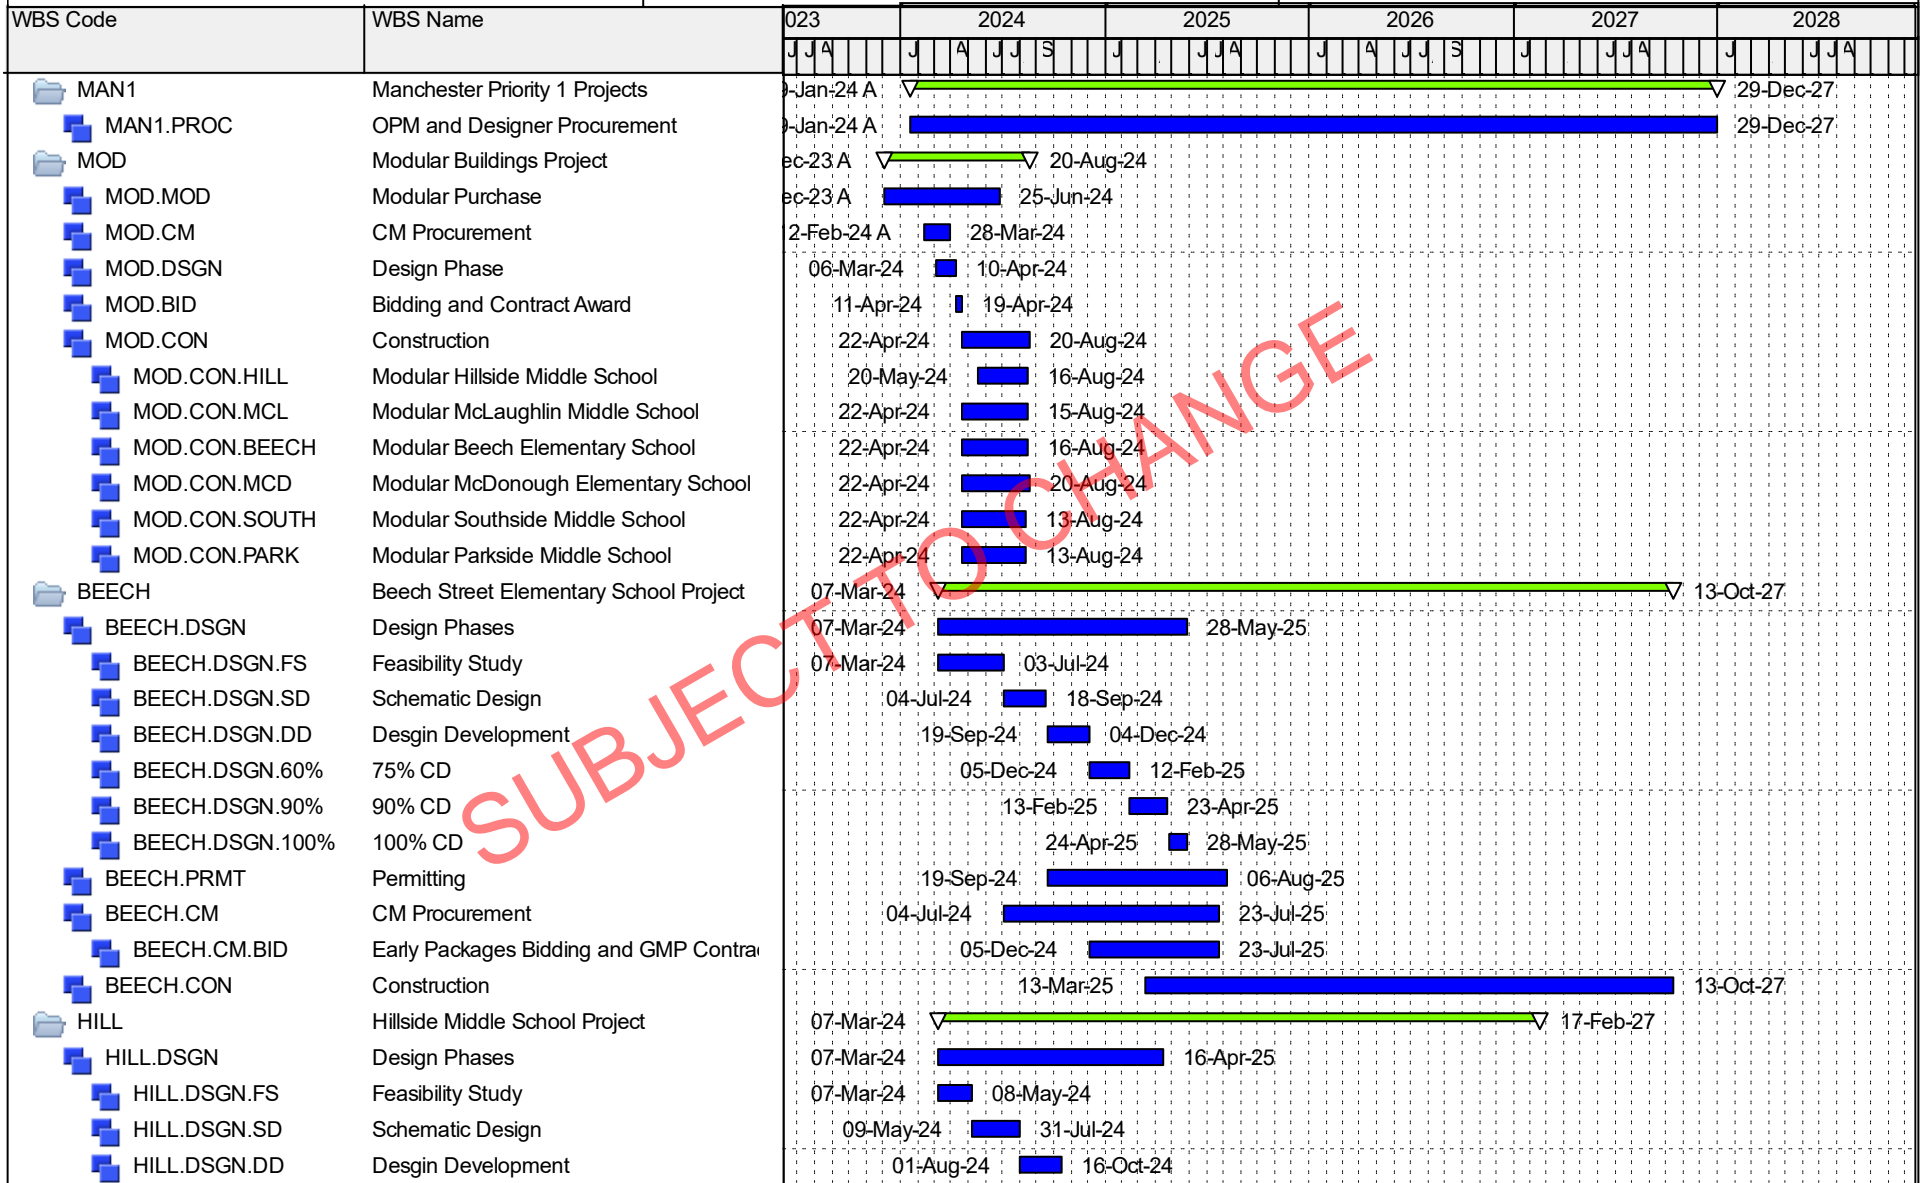


 All Projects
 WBS Elements below Project

PRIORITY 1 PROJECT SCHEDULE

06-Jun-24 18:11

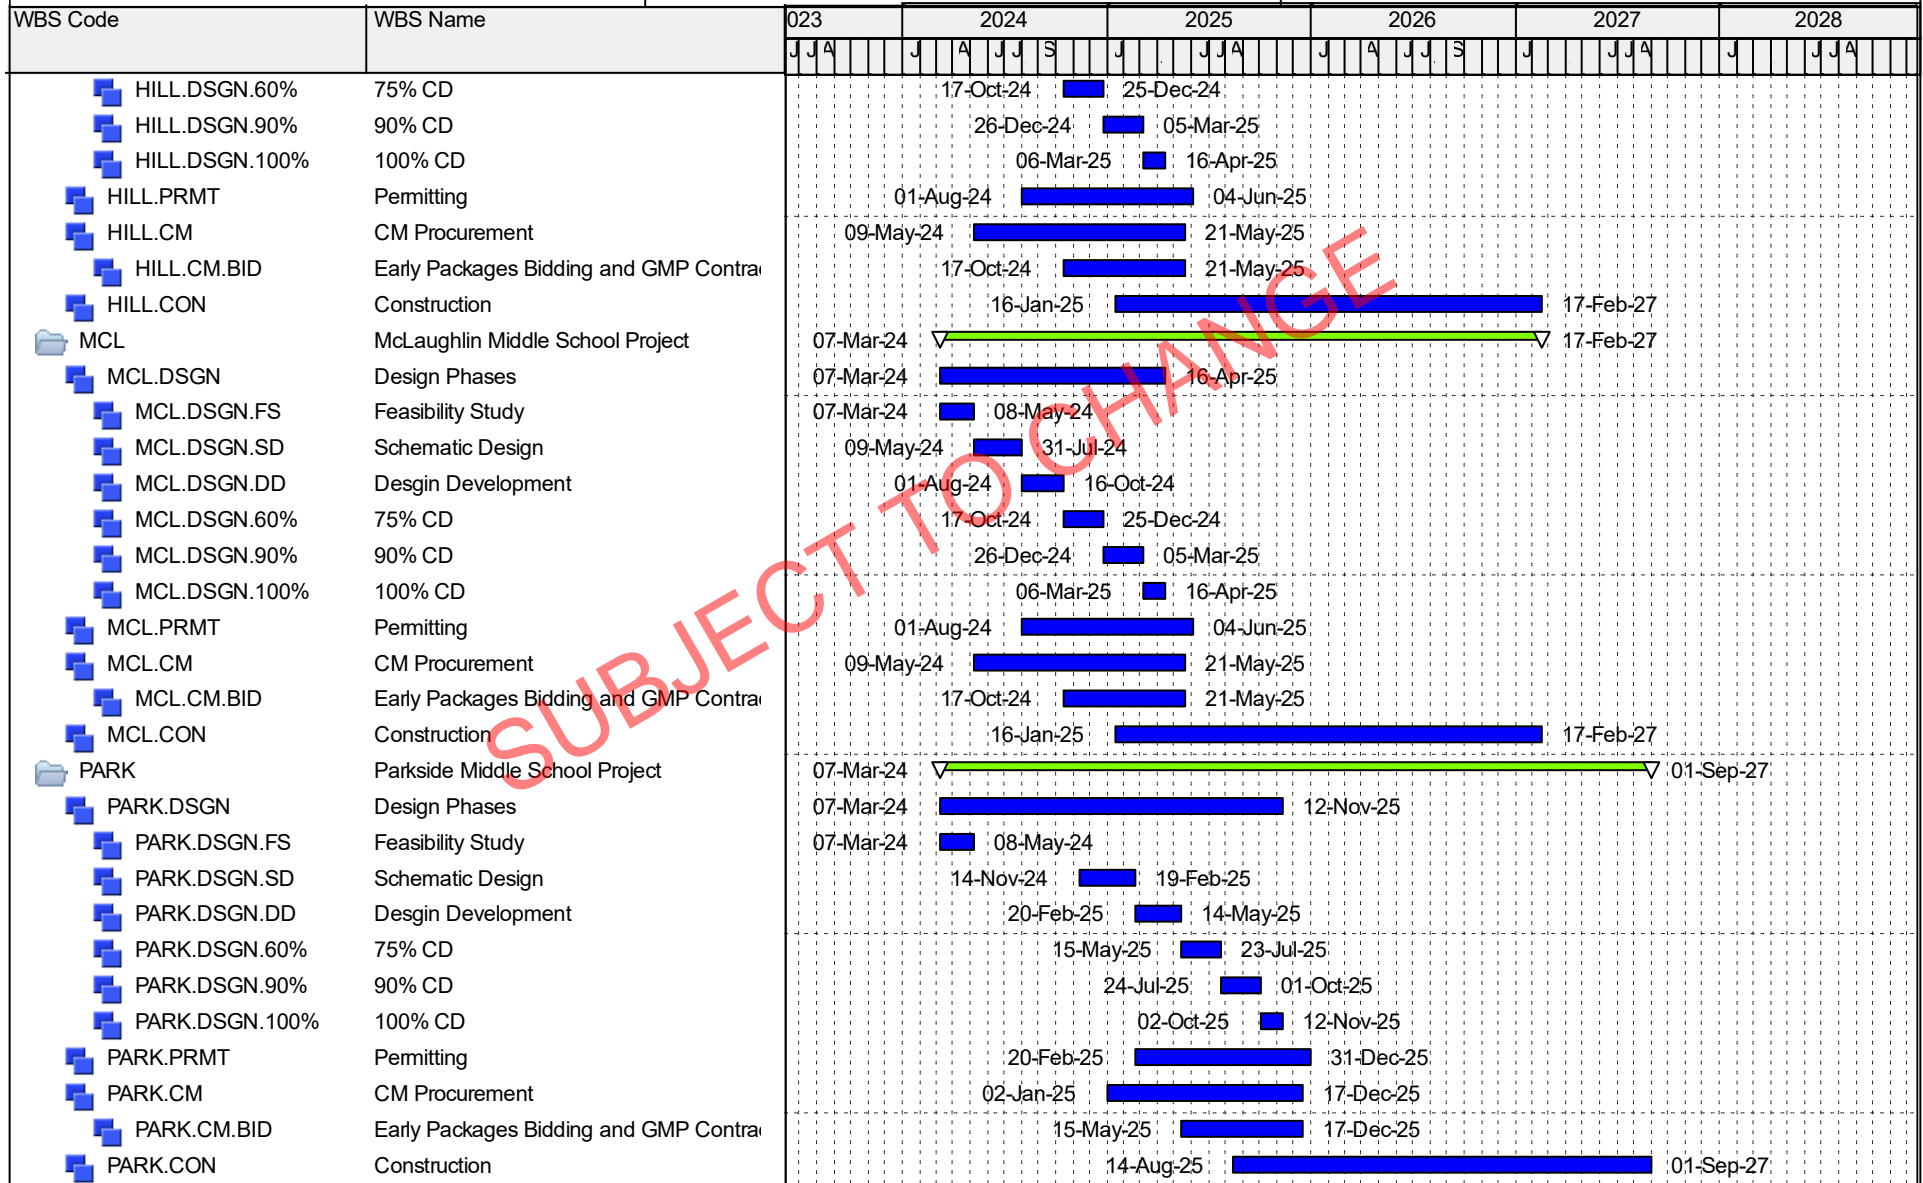


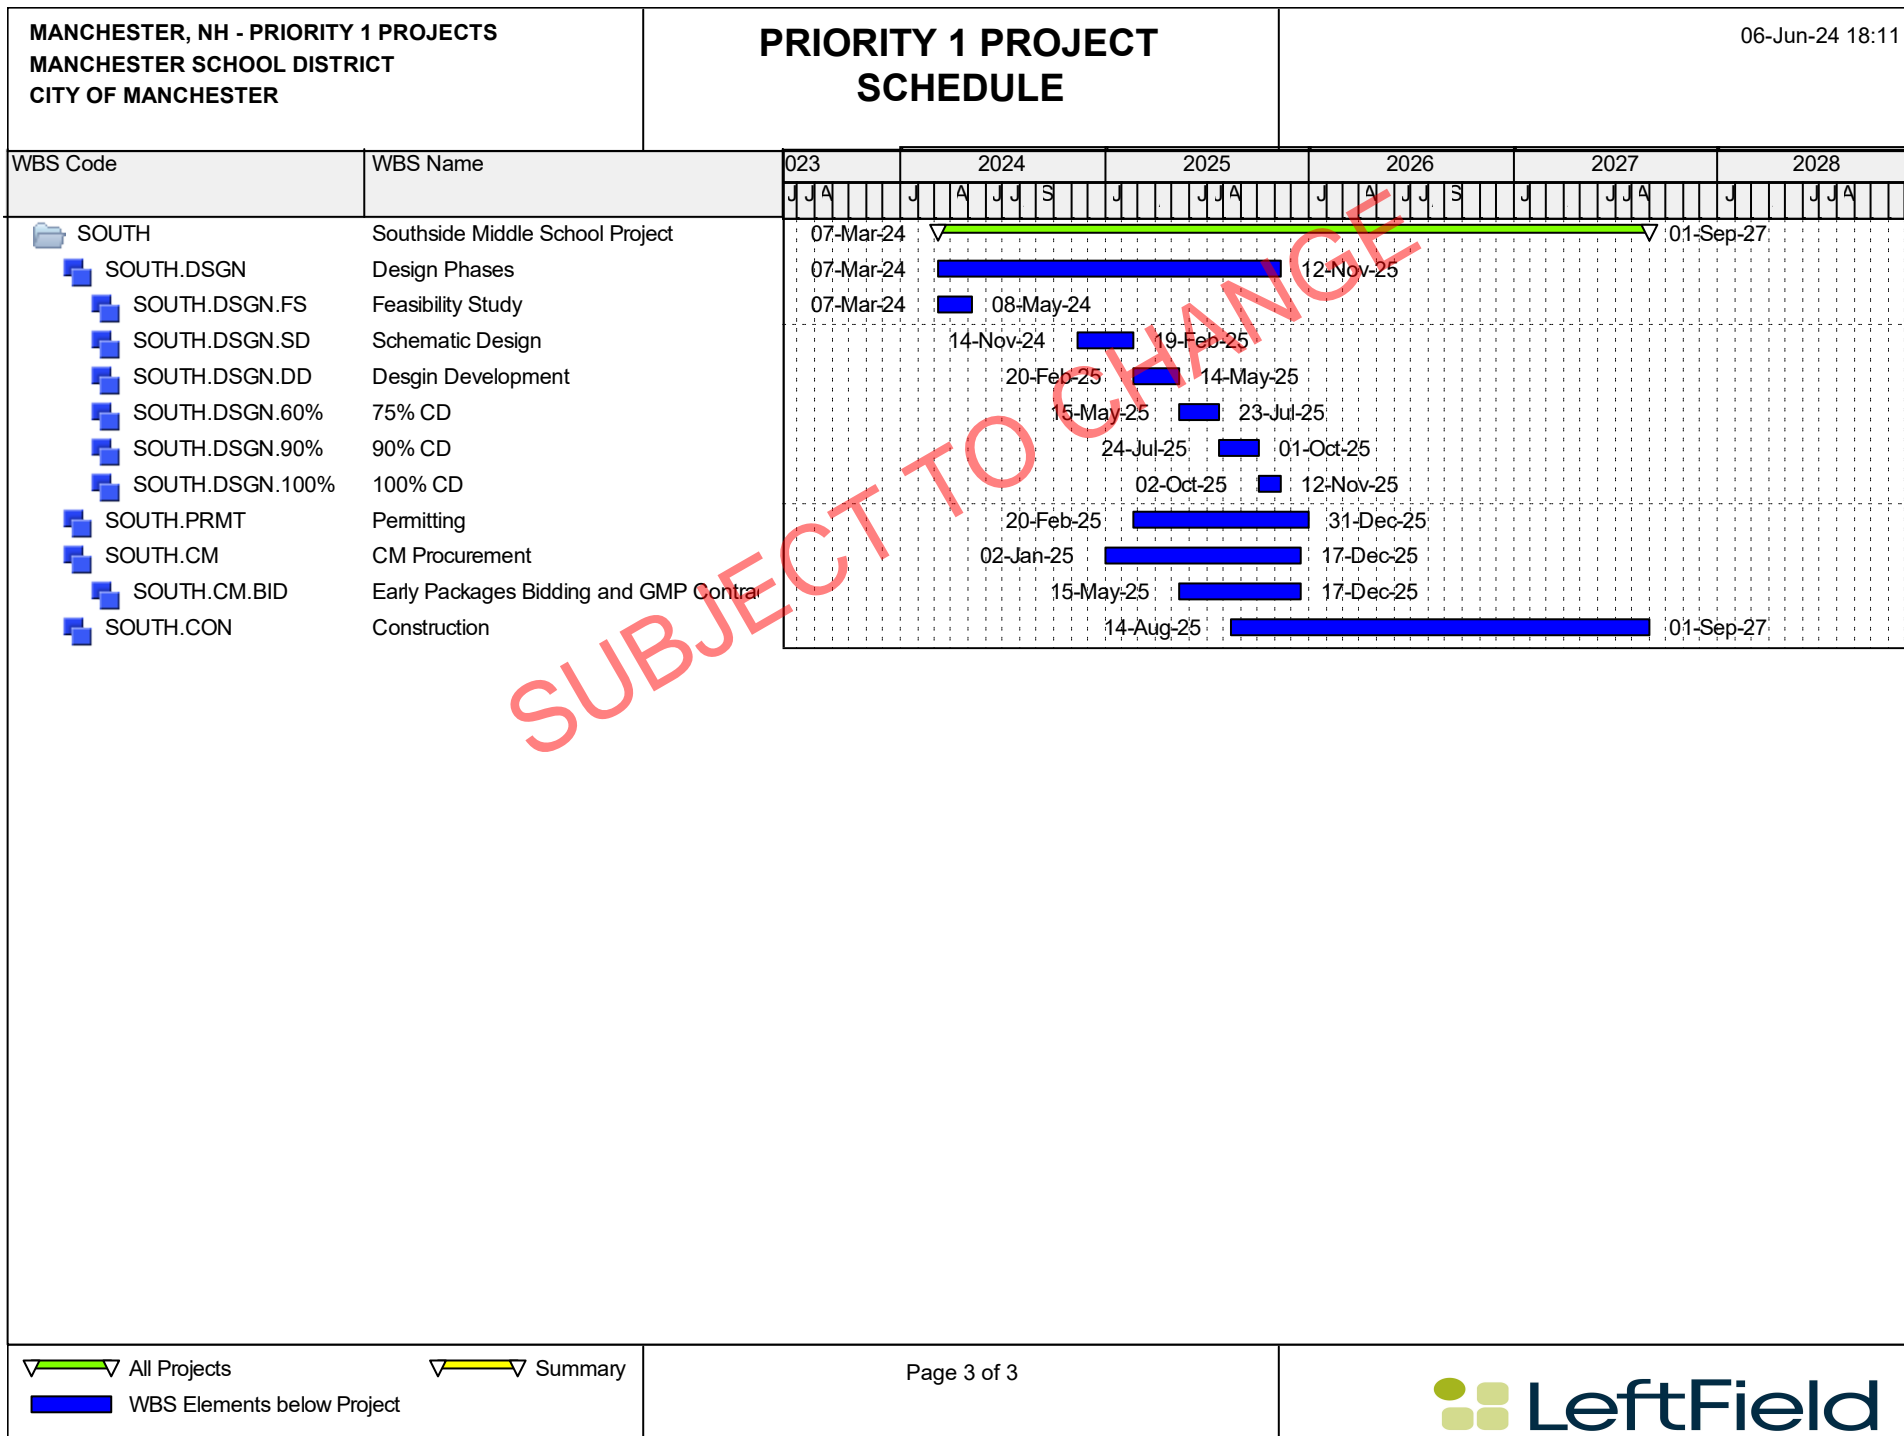

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

MODULAR BUILDING PROJECT
SCHEDULE

06-Jun-24 17:36


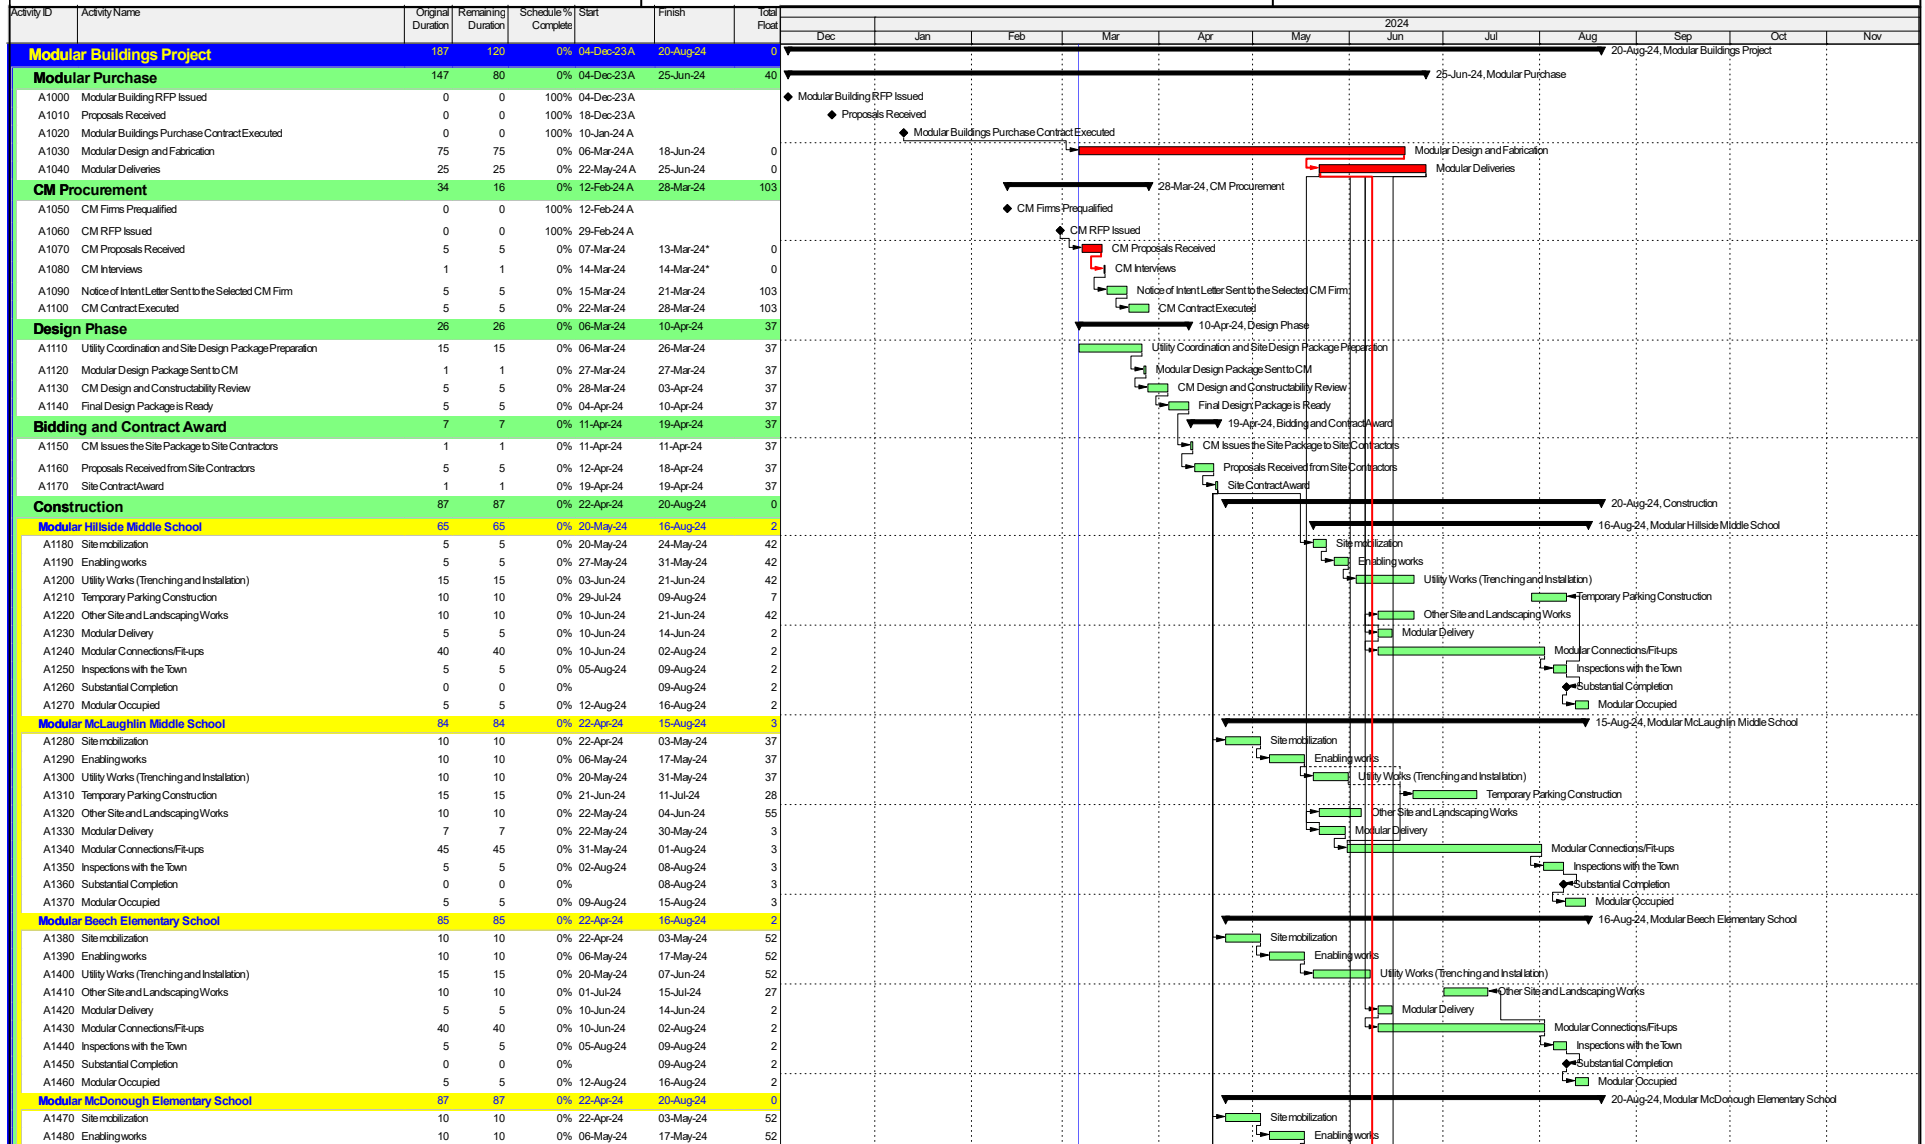


■ Actual Work
■ Remaining Work
■ Critical Remaining Work
◆ Milestone
➤ Summary

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

MODULAR BUILDING PROJECT
SCHEDULE


06-Jun-24 17:36

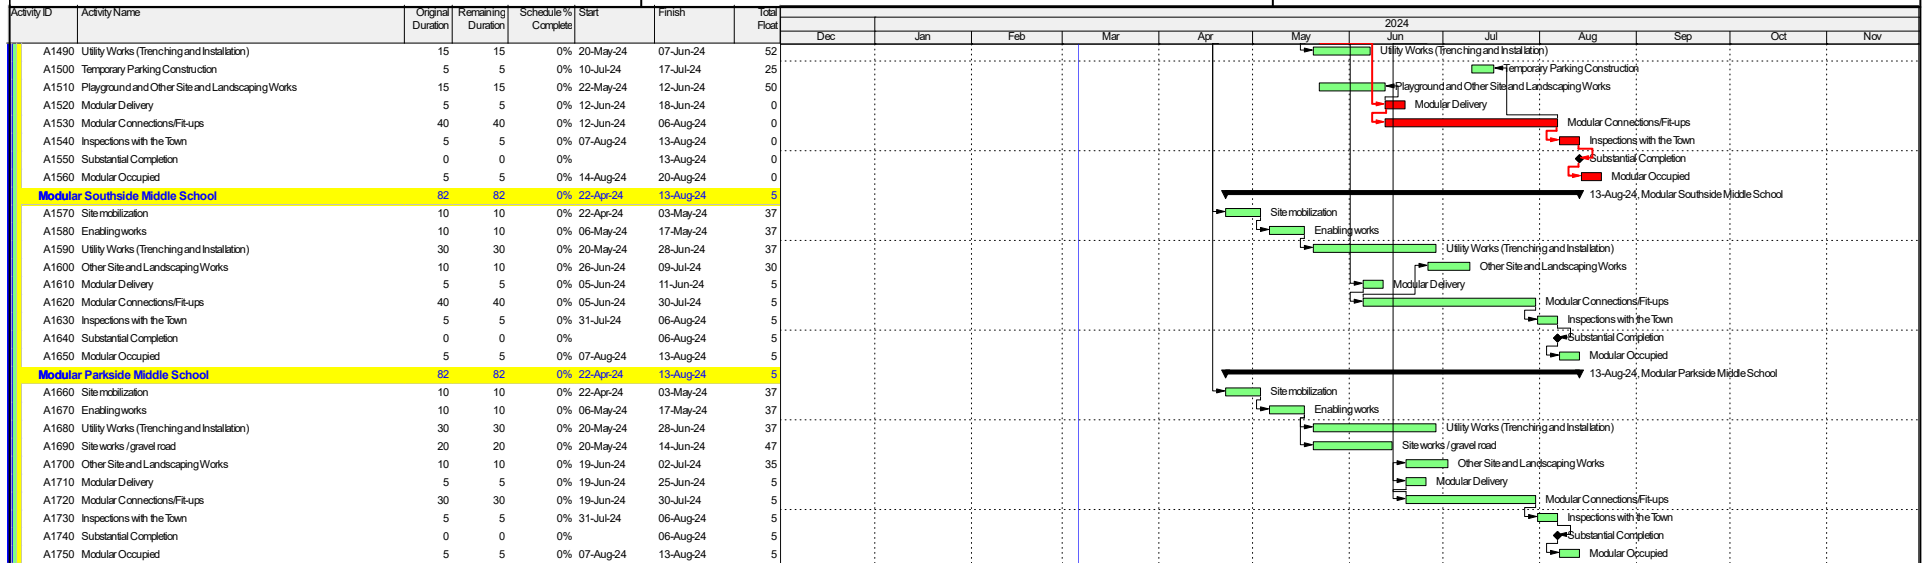

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

**BEECH STREET ELEMENTARY
SCHOOL PROJECT SCHEDULE**

06-Jun-24 17:51

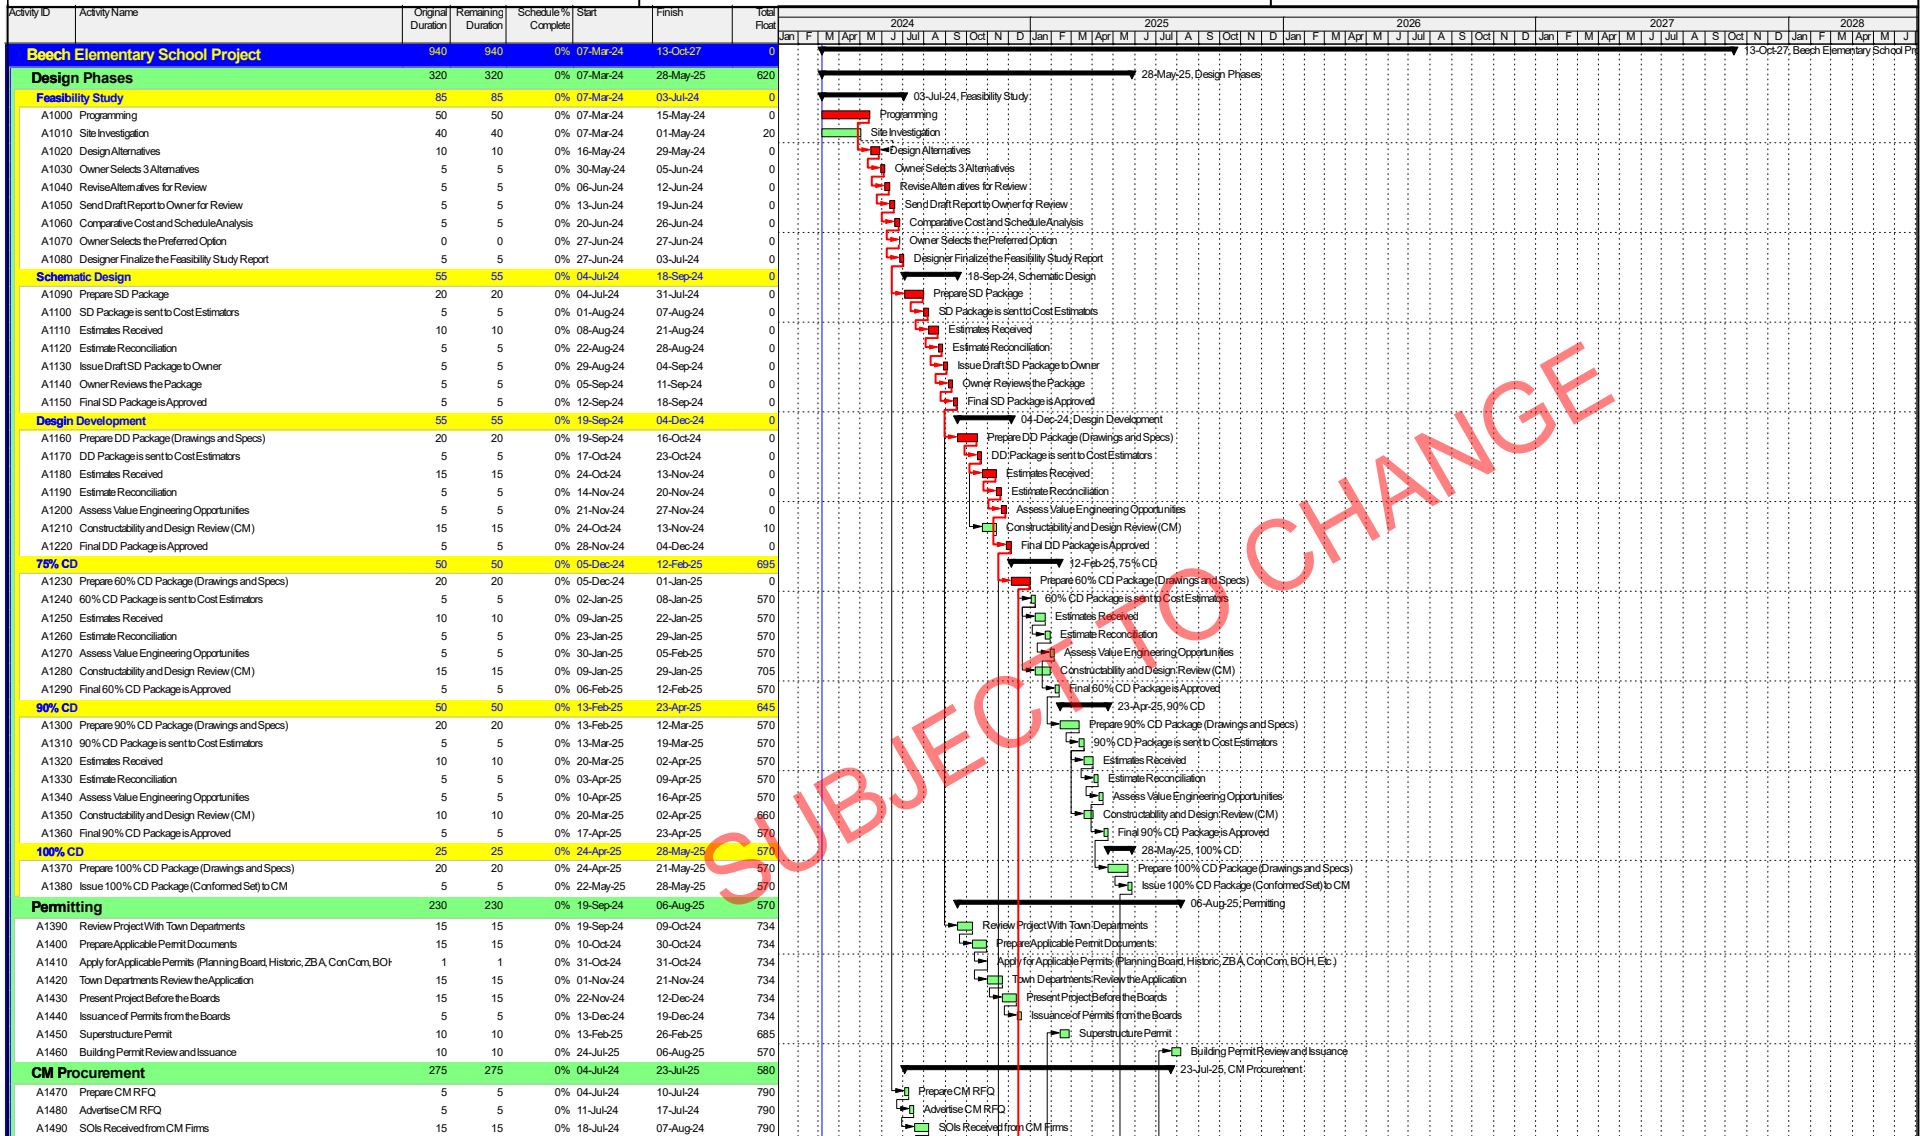


■ Actual Work
 ■ Remaining Work
 ■ Critical Remaining Work

◆ Milestone
 ▶ Summary

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

BEECH STREET ELEMENTARY
SCHOOL PROJECT SCHEDULE

06-Jun-24 17:51

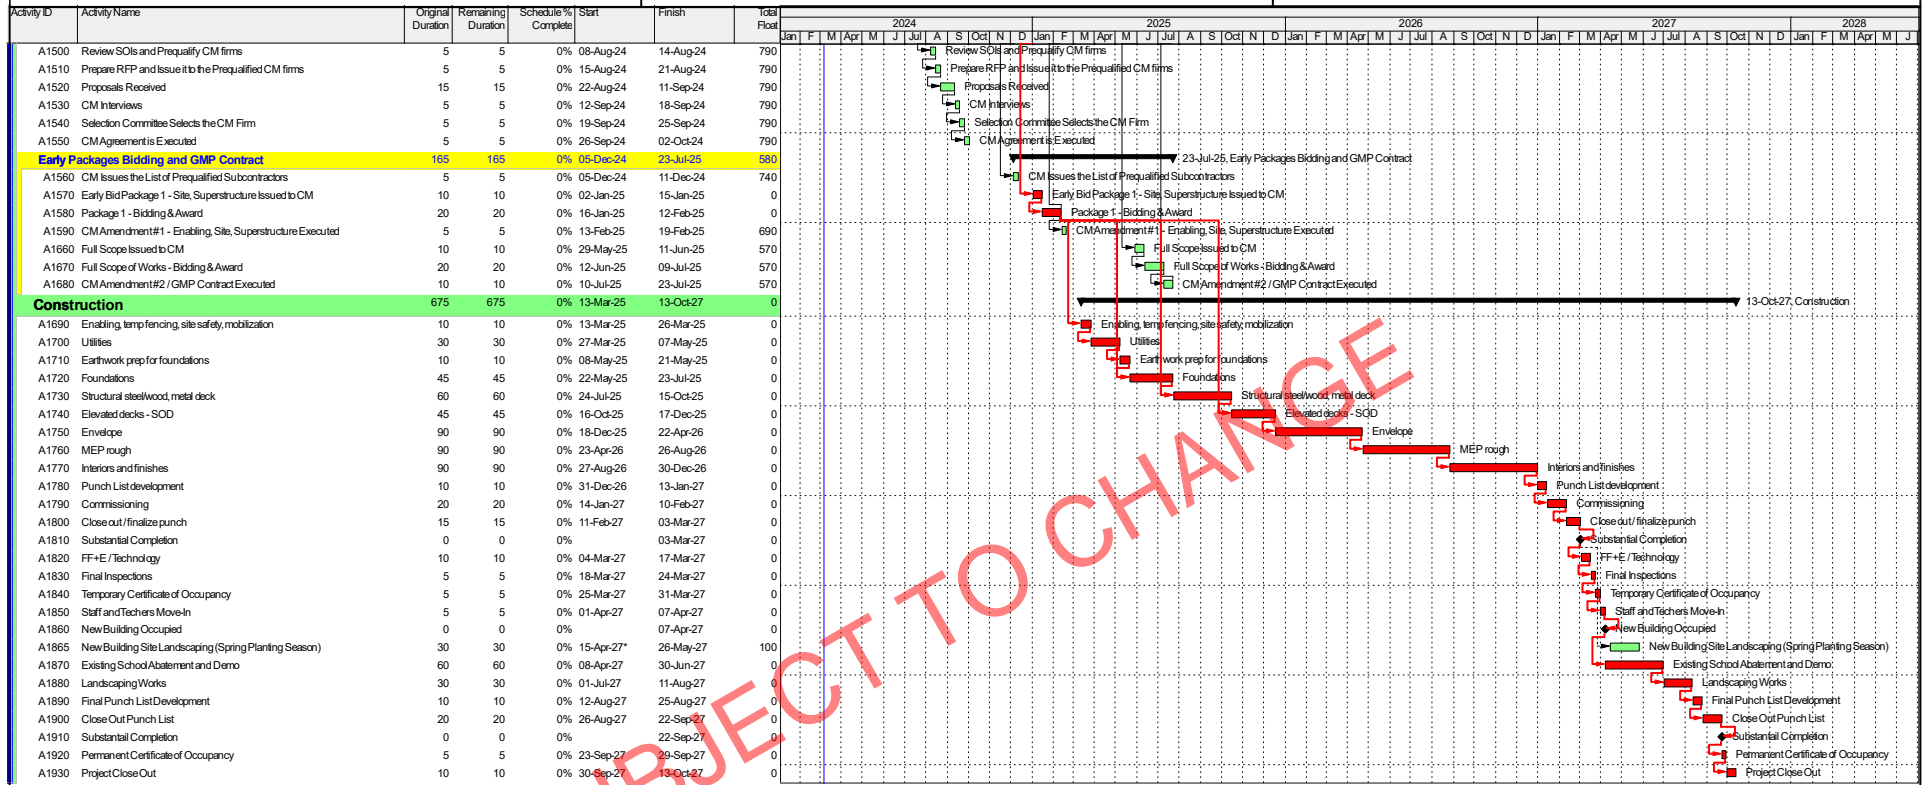


■ Actual Work
 ■ Remaining Work
 ■ Critical Remaining Work
 ◆ Milestone
 ➔ Summary

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

HILLSIDE MIDDLE SCHOOL PROJECT
SCHEDULE

06-Jun-24 17:56

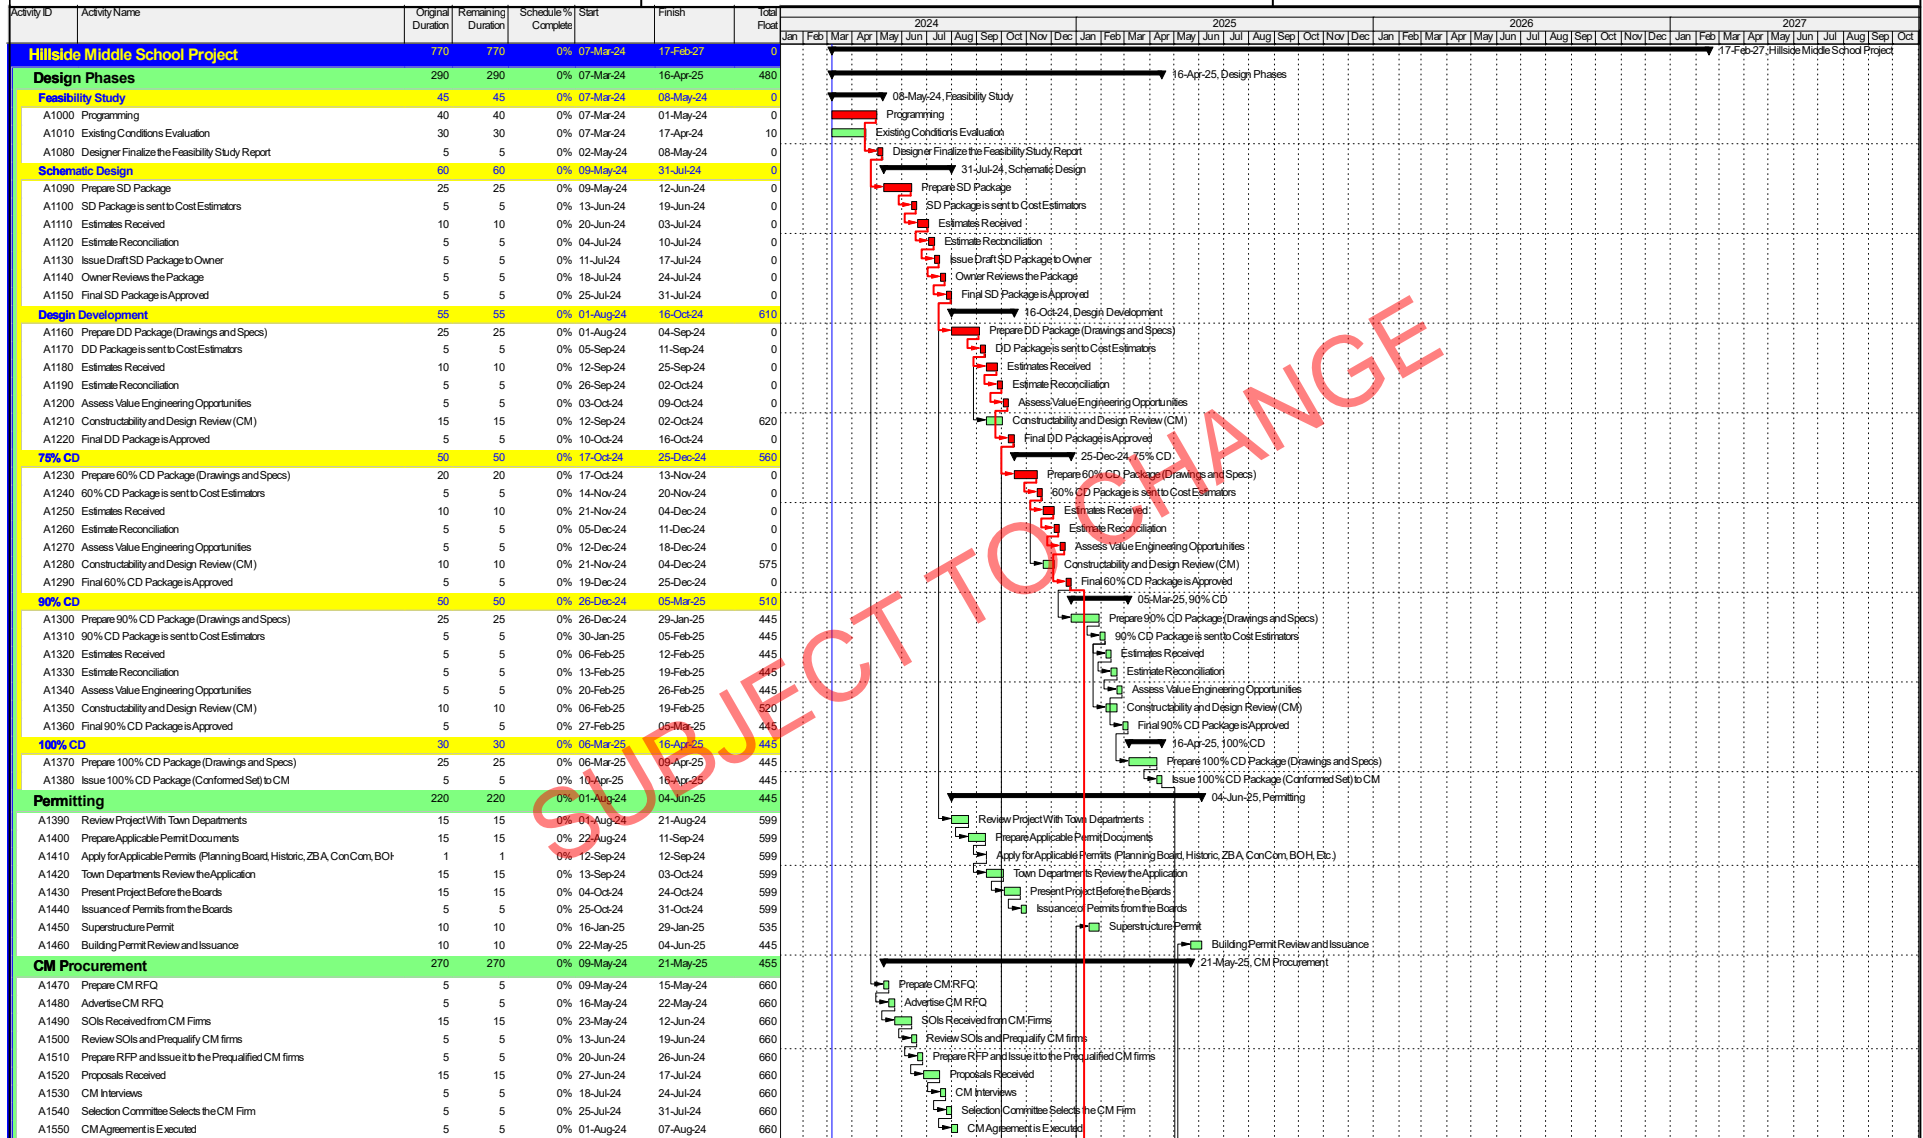


Actual Work
 Remaining Work
 Critical Remaining Work

Milestone
 Summary

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

HILLSIDE MIDDLE SCHOOL PROJECT
SCHEDULE

06-Jun-24 17:56

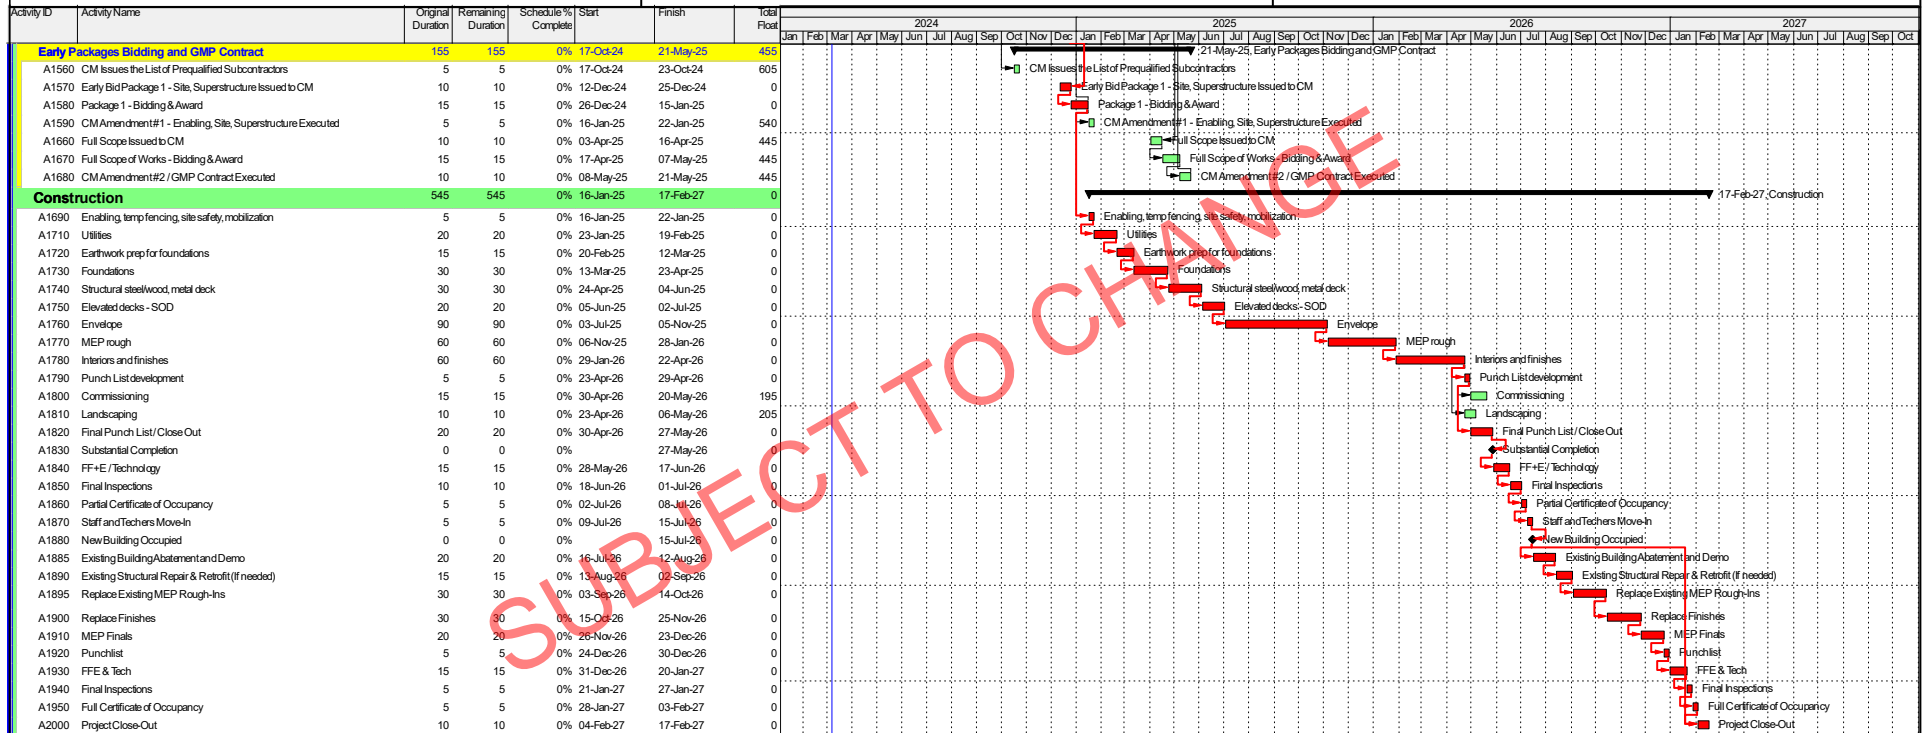

■ Actual Work
 ■ Remaining Work
 ■ Critical Remaining Work
 ◆ Milestone
 ➡ Summary

06-Jun-24 17:59




LeftField
THE RIGHT CHOICE IN PROJECT MANAGEMENT

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

MCLAUGHLIN MIDDLE
SCHOOL PROJECT SCHEDULE

06-Jun-24 17:59


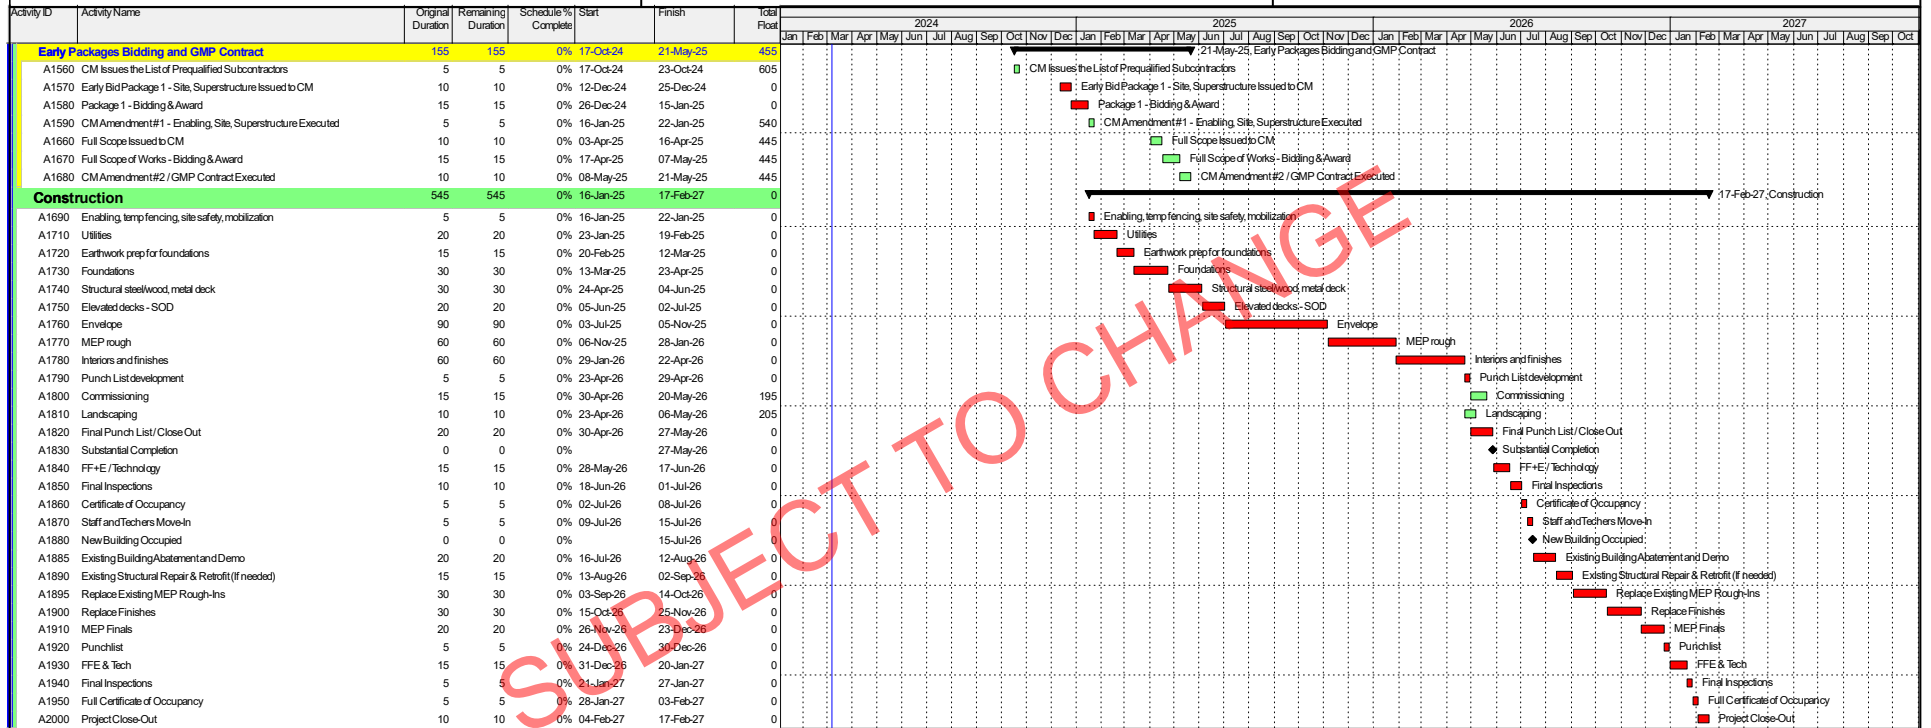


■ Actual Work
 ■ Remaining Work
 ■ Critical Remaining Work
 ◆ Milestone
 ▬ Summary

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

PARKSIDE MIDDLE
SCHOOL PROJECT SCHEDULE



06-Jun-24 18:02

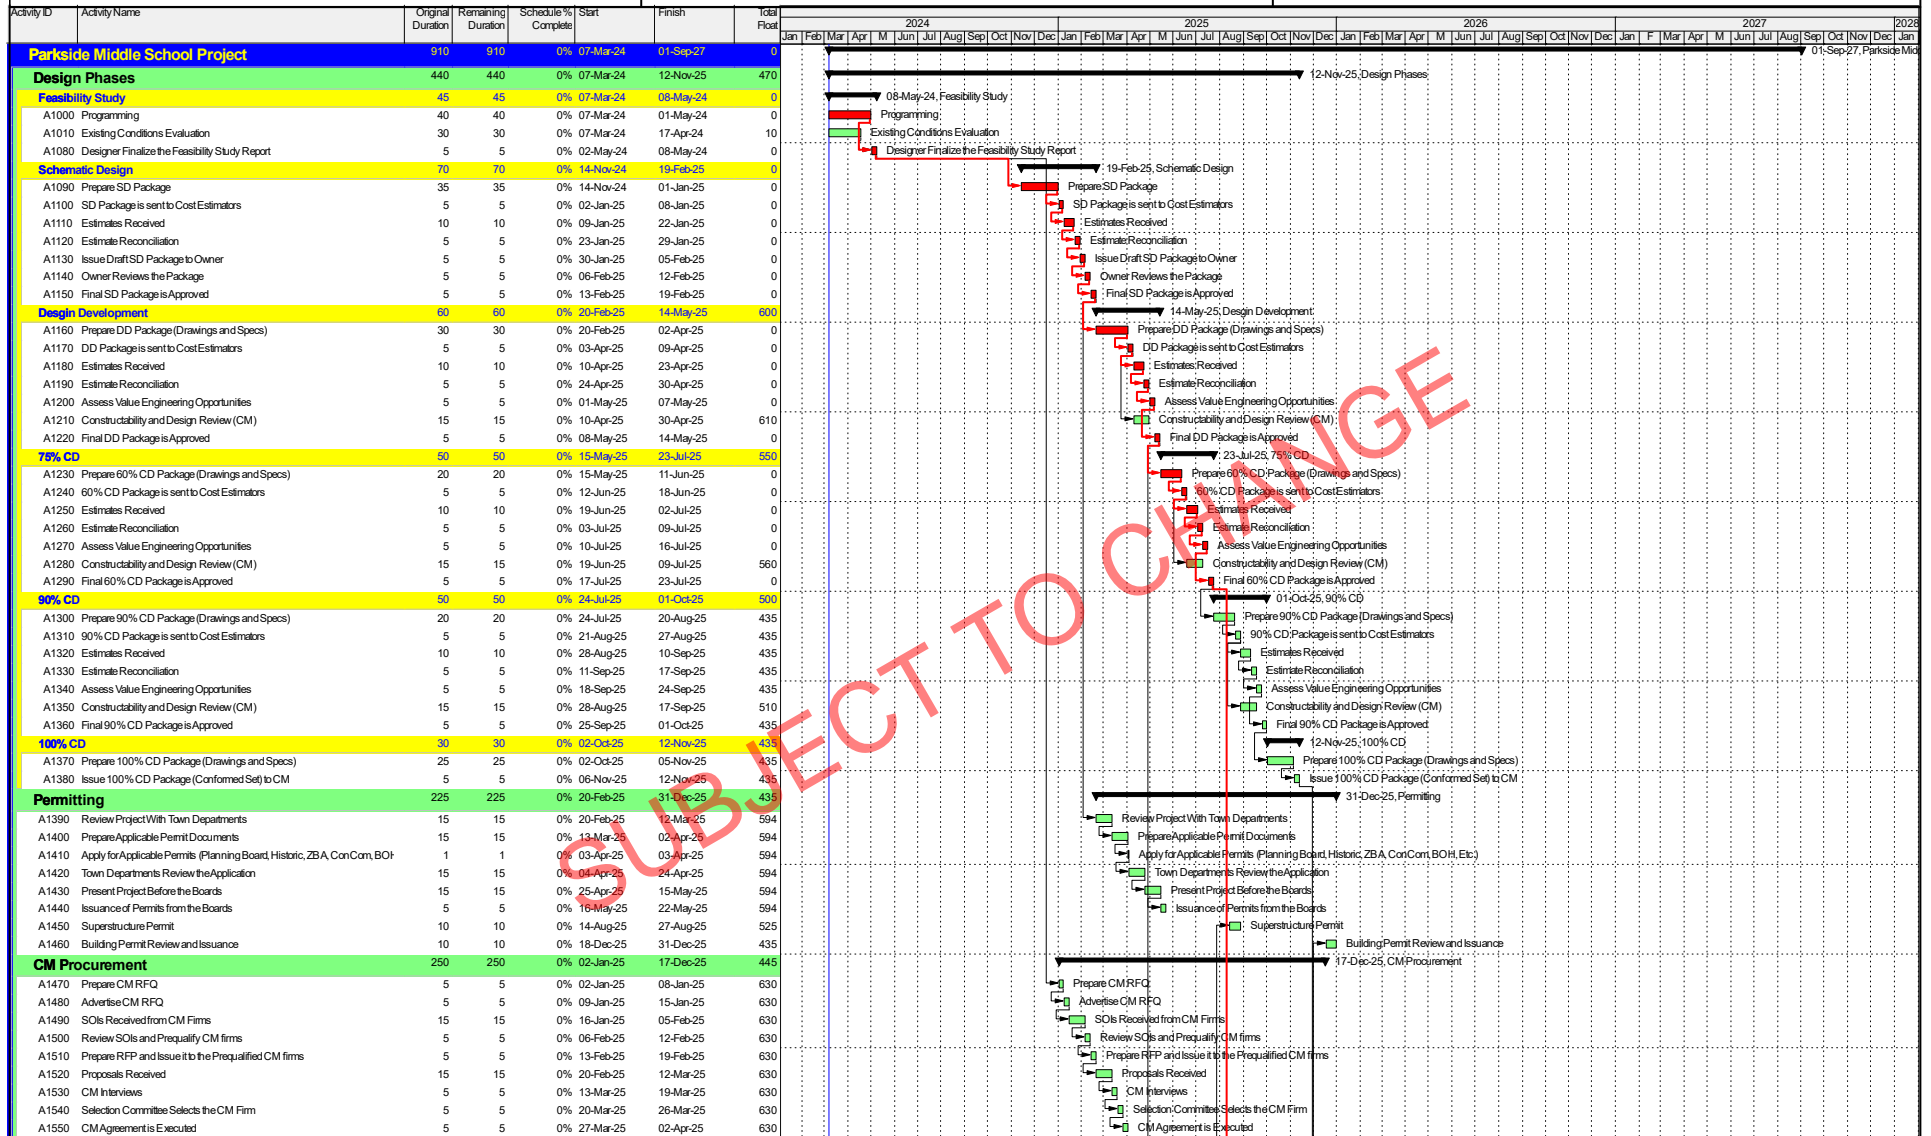

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

PARKSIDE MIDDLE
SCHOOL PROJECT SCHEDULE


06-Jun-24 18:02

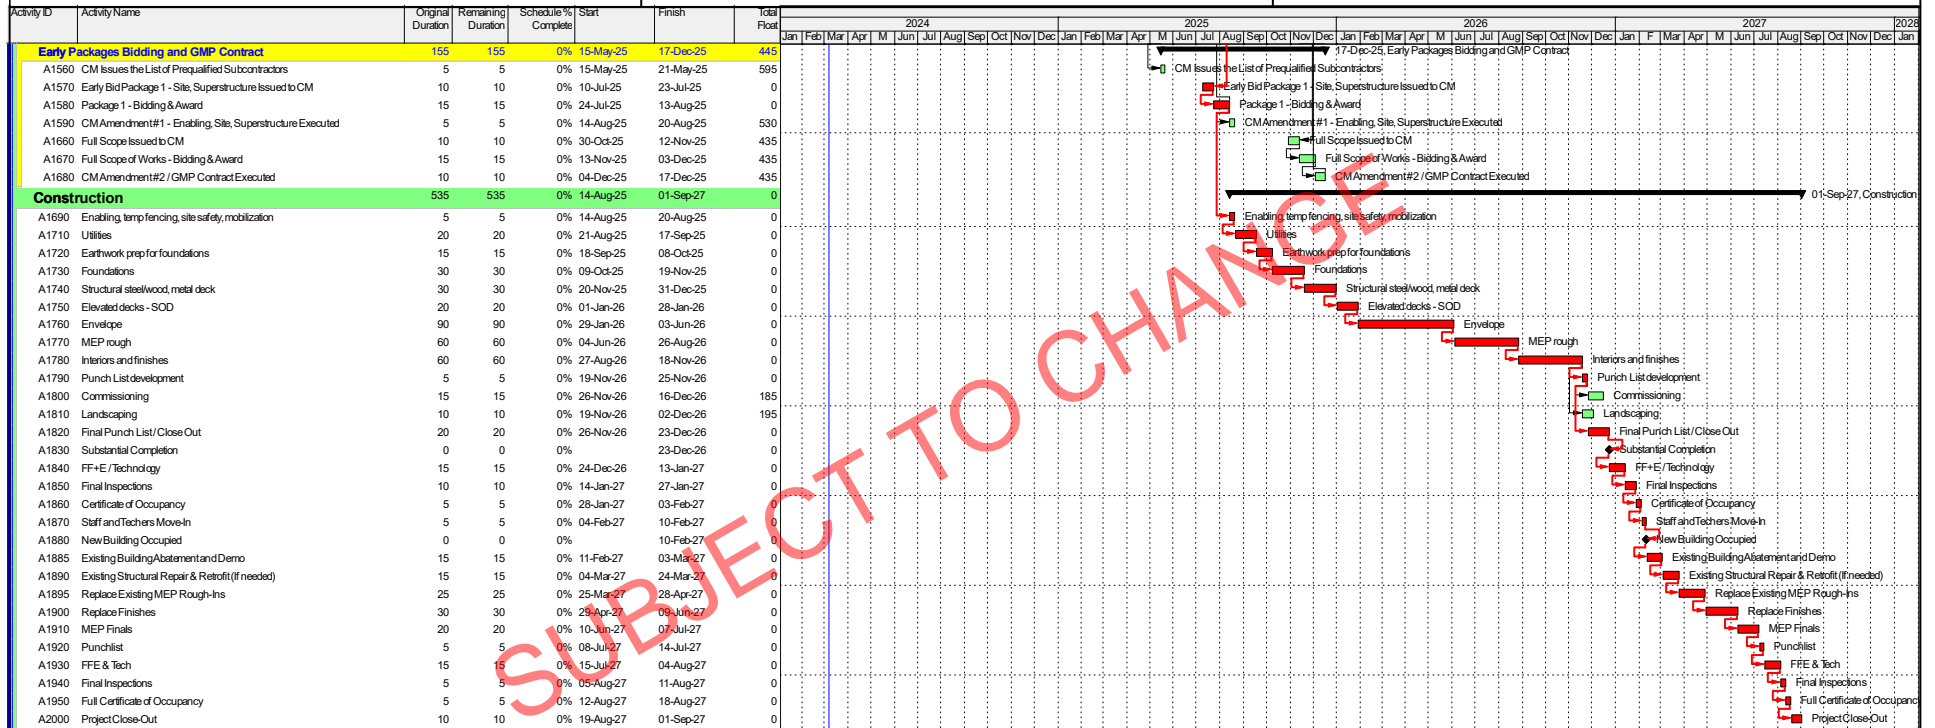

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

SOUTHSIDE MIDDLE
SCHOOL PROJECT SCHEDULE

06-Jun-24 18:04


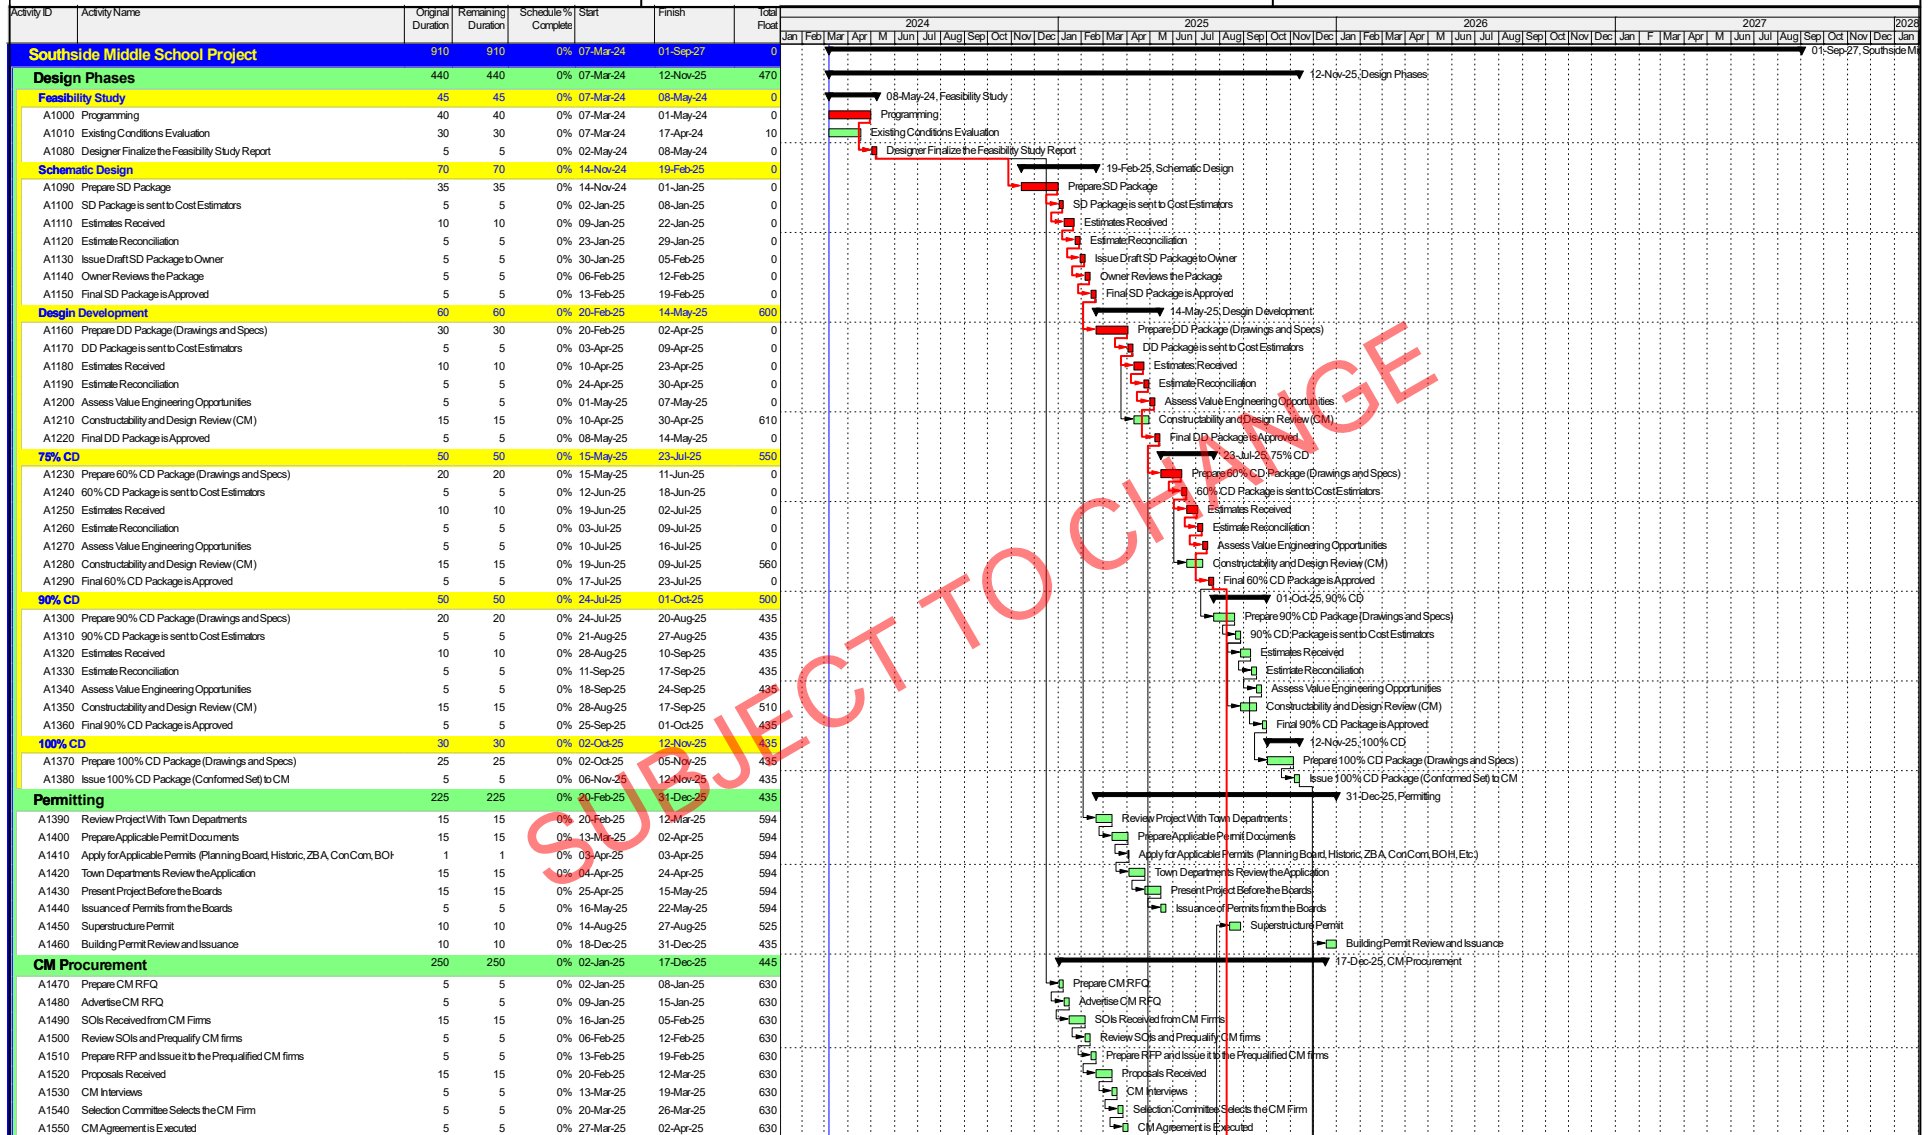


■ Actual Work
 ■ Remaining Work
 ■ Critical Remaining Work
 ◆ Milestone
 ➔ Summary

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

SOUTHSIDE MIDDLE
SCHOOL PROJECT SCHEDULE

06-Jun-24 18:04

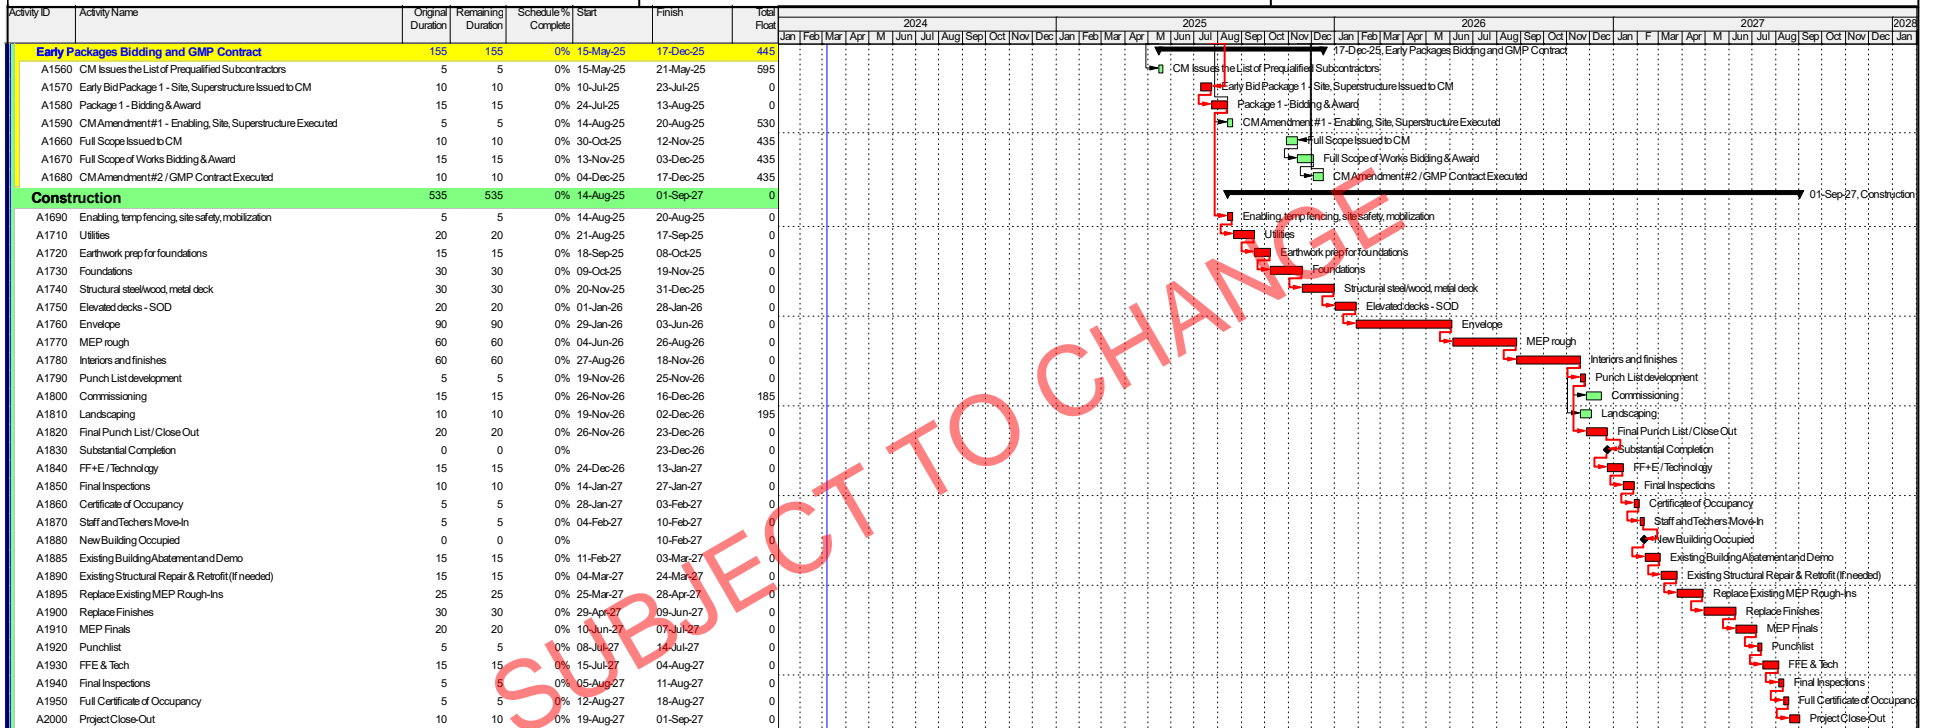

ATTACHMENT D

Modular Delivery Schedule



Updated 5/29/2024

Manchester Multi School Modulares Shipping Schedule

***** All Delivery Dates are Subject to Change Pending no
Mechanical Delays during Transport *****

<u>Scheduled Arrival</u>			
<u>Date</u>	<u># Units</u>	<u>School</u>	<u>Status</u>
5/23/2024	6	McLaughlin	Delivered
5/28/2024	6	McLaughlin	Delivered
5/30/2024	1	McLaughlin	Delivered
5/30/2024	5	Southside	Delivered
6/3/2024	6	Southside	Delivered
6/3/2024	1	Southside	Delivered
6/5/2024	1	Southside	
6/5/2024	3	Beech	
6/5/2024	3	Beech	
6/7/2024	3	Beech	
6/10/2024	1	Beech	
6/10/2024	8	McDonough	
6/11/2024	2	McDonough	
6/11/2024	1	Hillside	
6/12/2024	4	Hillside	
6/13/2024	3	Hillside	
6/17/2024	5	Hillside	
6/17/2024	2	Parkside	
6/18/2024	3	Parkside	
6/19/2024	4	Parkside	
6/20/2024	3	Parkside	
6/24/2024	1	Parkside	

**** All dates in green are subject to change pending on coordination with
site and transport****
